

(This SWPPP Template is for the **Common Plan** Permit Only, and
does **NOT** address SWPPP requirements found in the CGP.)

Common Plan SWPPP for Sobey Residence

Project Address: 3457 E Westview Trail
Park City, UT 84098

Midway Construction Company

599 N Main Street
Heber City, UT 84032

NOI Permit Number UTRH02849

April 19, 2021



When Complete Please email a copy of this document, a site map, and a completed NOI to
KChristiansen@summitcounty.org

Do not upload to e360

1. Project Information

Project Name: [Sobey Residence](#)

Project Address: [3457 E Westview Trail](#) [Park City, UT 84098](#)

Owner (or owner contact) : Mark and Paula Sobey

Owner Telephone Number: 408-807-7903

Owner Email Address: mark.sobey@coherent.com

General Contractor: [Midway Construction Company](#)

Contact Person: Gary Hill

Address: [599 N Main Street](#) [Heber City, UT 84032](#)

Telephone Number: 435-503-2600

Email Address: gary@mcchomes.com

Answering “yes” to the question below means the project is not eligible for this permit.

Is the project in Indian Country?

Yes

No

Answering “no” to the question below means the project is not eligible for this permit.

Is the project a residential building on a single lot and disturbing one acre or less?

Yes

No

2. Pollution Sources/Best Management Practices

Answer yes or no whether the following features are located at your site. If yes, select the BMP(s) that will be used to protect each feature. If no, continue to the next question. Attach necessary illustrated details for proper installation in Appendix G, and show locations of all controls on Site Map in Appendix A.

- 2.1 Is there a SWPPP sign on site?** (see permit part 1.10) **Yes** **Required**
The sign must include the UPDES tracking number, the owner or general contractor name, phone number and email, and if the SWPPP is on-line, instructions on how to view it. The size requirement is to be readable from a publicly accessible point.
- 2.2 Will there be construction dewatering on the site?** (see permit part 2.7) **Yes** **No**
BMP(s): Dewatering of the construction area is needed and a separate dewatering permit has been obtained to treat and discharge water. *Construction Dewatering (if discharged offsite) must be covered by UPDES Permit UTG070000.*
 Water from the dewatering of the construction area will be infiltrated on site.
- 2.3 Will there be non-storm water discharges on the site?** (see permit part 1.3) **Yes** **No**
Allowable discharges include: Flushing of drinking water or irrigation water (not including wash or cleaning waters), water used for dust control, spring water or groundwater not exposed to construction activities, water from emergency fire-fighting activities, and water from foot drains not exposed to construction activities. (see permit part 2.4.5 & 2.9).
Please list all anticipated non-storm water discharges: [Click here to enter text.](#)

What will you do to manage the non-storm water discharges? *Please list direct discharges, contained non-storm water discharges, and discharges that are treated separately.*

- BMP(s):** All non-storm water discharges are listed as allowable per permit part 1.3 and discharged
 All non-storm water discharges that are not allowed are properly contained (see questions 2.12 and 2.16)
 All non-storm water discharges that are contaminated with sediment only (free of chemicals, oils, etc.) will be treated in a sediment basin or equivalent (see permit part 2.8.1).
 Other: [Click here to enter text.](#)

2.4 **Is it possible for the total area of disturbance to be phased, minimizing the total exposure of disturbed soil at one time?** (see permit part 2.3.1) Yes No
If disturbance can be minimized please show the locations on the site map and summarize (here) where disturbances will be delayed for some of the disturbed area: [Click here to enter text.](#)

2.5 **What perimeter controls will be used to prevent sediment from leaving the site?** (permit part 2.1.2 & 2.3)
BMP(s): Silt Fence Berms
 Vegetative Buffer Cut-Back-Curb
 Staked straw Wattles (Fiber Rolls) Weighted Wattles
 Other: [Click here to enter text.](#)

2.6 **Are surface waters located within 30 feet of your project's earth disturbances?** Yes No
Note: *A 30' natural vegetative buffer MUST be maintained by water bodies. If a buffer less than 30' is used, you must demonstrate that the additional controls offer the same protection as a 30' natural vegetative buffer, and select the reason for exemption below. (see permit part 2.3.5)*
BMP(s): 30' Natural Vegetative Buffer
 If less than 30' Natural Vegetative Buffer select additional Controls:
 2 Silt Fence Barrier 2 Straw Wattle Barriers (Fiber Roll)
 Other: [Click here to enter text.](#)

2.7 **Are there critical or sensitive areas (such as preservation of the drip lines around trees, wetlands, buffer zones by water bodies, etc.) located on or adjacent to the site?** (see permit part 2.2) Yes No
BMP(s): Separate and isolate with environmental fencing
 Other: [Click here to enter text.](#)

2.8 **What track out control will be used to prevent dirt from being tracked on streets as vehicles leave the site?** (see permit part 2.4.1)
BMP(s): Track Out Pad Cobble Gravel
 Rumble Strips Wash Down Pad Delivery Pad
 Restricted Site Selective Access During Dry Weather (Dry soil) Access
 Other: gravel or wood chips are identified on CMP

2.9 **Do you have storm drain inlets on or down gradient of this site?** (see permit part 2.1.3) Yes No
Protection must address the curb inlet opening (throat) as well as the grate.

Where is/are the nearest downstream inlet(s) and how will you protect them: There are no inlets anywhere nearby

- BMP(s):** Rock/Sand-filled Bags Drop Inlet Bags
 Filter Fabric Gravel or Sand filled Wattles
 Proprietary inlet devices
 Other: Click here to enter text.

2.10 Will curb ramps be used at the site? (see permit part 2.4.2) **Yes** **No**

If curb ramps are used it must be done with material [not dirt] that will not wash away in storm water.

- BMP(s):** Crushed Rock Wood/Steel Ramps
 Other: Click here to enter text.

2.11 Will there be stockpiles or spoil piles on the site? **Yes** **No**

Note: Select "Contained by other BMP" if another BMP on your site will contain runoff from the stockpiles. Materials that can be transported with precipitation must not be placed in the street. (see permit part 2.1.1)

- BMP(s):** Surrounded by Silt Fence Surrounded by Staked Straw Wattles
 Covered with Tarp Temporary – Removed same day
 Contained by other BMP. Explain: Silt fence is already planned downgradient of all construction activity, and will therefore also contain runoff from stockpiles
 Other: Click here to enter text.

2.12 Does the project include installation of concrete, masonry, stucco, and paint (water based)work in this project? (see permit part 2.4.5 & 2.9.1) **Yes** **No**

Wash water must be contained, the solids dried, and disposed of at a landfill.

- BMP(s):** Lined Depression Steel Dumpster
 Regional Washout (per development)
 Other: Click here to enter text.

2.13 How will solid waste be dealt with on the site? (see permit part 2.4.3)
Light trash in uncovered dumpsters can blow out and scatter with wind and rain may fall on uncovered leachable material in the dumpster and leak out the bottom causing pollutants to escape.

- BMP(s):** Bag Lightweight Trash Leak Proof Dumpsters
 Receptacles with Lids Other: Click here to enter text.

2.14 Will there be a need to dispose of solvents, oil, fuel, etc. liquid waste? (see permit part 2.9) **Yes** **No**

- BMP(s):** Contained and Removed from the site Collected for Reuse
 Other: Click here to enter text.

2.15 How will sanitary waste be handled on the site? (see permit part 2.4.4)

- BMP(s):** Portable Toilet(s) (must be staked down on dirt surface & 10' from curb)
 Onsite or Adjacent Indoor Bathrooms
 Portable Toilet Secondary Containment (secured down with straps to heavy weights)
 Other: Click here to enter text.

2.16 How will you minimize the discharge of pollutants from spills and leaks? (see permit part 2.8.3)

- BMP(s):** Use of drip pans Offsite fueling, and maintenance
 Spill kit Spill response plan.

Other: Click here to enter text.

2.17 Will there be a need to store construction materials on site? (see permit 2.8.2) **Yes** **No**
Minimize the exposure of materials with a pollution risk (certain building and landscaping materials, fertilizers, pesticides, herbicides, detergents).

BMP(s): Covering Erodible or Liquid Materials Secondary Containment
 Strategic Storage and Staging Stored off-site
 Enclose them in a weather proof shed.
 Other: Click here to enter text.

2.18 Does your site have steep slopes (greater than 70%)? (see permit part 2.3.2) **Yes** **No**

BMP(s): Erosion Control Blanket Avoid Disturbance on slope
 Seeding Hydroseed
 Mulch Takifiers
 Other: Click here to enter text.

2.19 Are there site conditions that cause storm water flows with highly erosive velocities? (see permit parts 2.3.3 and 2.3.4) **Yes** **No**

Flows must be controlled to minimize sediment transport.

BMP(s): Gravel Check Dam Straw Wattles (Fiber Rolls) Check Dam
 Divert Flows around the Site Armored channel (riprap, geotextile, other)
 Other: Click here to enter text.

2.20 How will you reduce storm water volume to minimize sediment transport, channel and stream bank erosion? (see permit parts 2.3.4 and 2.3.3)

BMP(s): Utilize basin, depression storage of storm water, cut back curb, or other to hold and infiltrate.
 Prevent heavy equipment (as much as possible) from compacting soil so storm water will infiltrate easier.
 Rip soil after heavy equipment has caused compaction.
 Other: Click here to enter text.

2.21 Is there a need for dust control on the site (regulatory or for practical reasons)? **Yes** **No**

BMP(s): Wetting with Water Cover dirt piles with a tarp
 Use Magchloride, Calcium Chloride or Lignan Sulfonate
 Stabilize surface with mulch, gravel or other surface cover
 Other: Click here to enter text.

2.22 Will there be disturbed areas on the site that will need to be temporarily stabilized before the project is completed? (see permit part 2.6) **Yes** **No**

Places that are disturbed and then left for over 14 days with no activity, must be temporarily or permanently stabilized.

BMP(s): Bark or other mulch Hydro-mulch Seeding
 Tackifier Staked netting with straw mulch
 Other: Click here to enter text.

2.23 Will the house be sold without any landscaping? Yes No

If so, how will you leave the site for the new home owner so sediment will be contained on site until the home owner completes landscaping? *(the permit can be terminated when the owner occupies the house even though the site is not stabilized).*

- BMP(s):**
- Mulching/Hydro-mulching
 - Swales
 - Silt Fence
 - Wattles
 - Cut-Back-Curb
 - Seeding
 - Vegetated Buffer
 - Grade Front-Yard Lower than Sidewalk
 - Other: [Click here to enter text.](#)

3. Sequence of Construction Activity

Type of Construction Activity	Approximate Date Range
Start/End of the Project	June 2021 – November 2022
Excavation activities	June – August 2021
Foundation/Footings	August - September 2021
Backfill	September 2021
Erection of Building	September 2021 - November 2022
Utility Lines installed	July 2021
Site Stabilization	September – October 2021
Landscaping	Summer 2022

4. Site Map

On a blank page (or include a page from the architectural drawings that show site layout and dimensions), please draw a map (and place this map in Appendix A) showing the layout of the site including locations of:

1. boundaries of project/property
2. boundaries of disturbance (including areas outside of property boundaries)
3. show slopes on site (if there are steep areas show steep areas)
4. location of structures/facilities
5. locations of :
 - a. stockpiles for soils and materials
 - b. construction supplies
 - c. portable toilets
 - d. garbage/trash containers
 - e. egress points/track out pads
 - f. concrete washout pits or containers

6. water bodies, wetlands, natural vegetative buffers
7. placement of all BMPs, perimeter, erosion control, sediment control, inlet protection, etc.
8. storm water inlets and storm water discharge points (where storm water drains off the site)
9. areas that will be temporarily or permanently stabilized on the site
10. areas where disturbances will be delayed to minimize total exposed surface at one time.

5. Potential Sources of Pollutants

Fill out the table below with a pollution prevention method. **Examples include:** Strategic Storage, designated washout area, use only as needed (for fertilizers, etc), or Not Applicable.

Material/Chemical	Storm Water Pollutants	Common Location*	Pollution Prevention Methods
Pesticides (insecticides, fungicides, herbicides, rodenticide)	Chlorinated hydrocarbons, organophosphates, carbamates, arsenic	Herbicides used for noxious weed control	NA – if needed will be stored offsite. Spill plans in place when brought to site.
Fertilizer	Nitrogen, phosphorous	Newly seeded areas	Applied when no rain is forecast. Stored offsite. Prevent from leaving site with vegetative buffer.
Plaster	Calcium sulphate, calcium carbonate, sulfuric acid	Building construction	Captured by onsite stormwater retention, prevented from leaving site, spills cleaned immediately
Cleaning solvents	Perchloroethylene, methylene chloride, trichloroethylene, petroleum distillates	No equipment cleaning allowed in project limits	NA – equipment will be cleaned off site
Asphalt	Oil, petroleum distillates	Streets and roofing	Stored offsite, will be immediately paved and compacted
Concrete	Limestone, sand, pH, chromium	Curb and gutter, building construction	Concrete washout
Glue, adhesives	Polymers, epoxies	Building construction	Spill prevention and cleanup plan
Paints	Metal oxides, Stoddard solvent, talc, calcium carbonate, arsenic	Building construction	Spill prevention and cleanup plan
Curing compounds	Naphtha	Curb and gutter	NA
Wood preservatives	Stoddard solvent, petroleum distillates, arsenic, copper, chromium	Timber pads and building construction	Spill prevention and cleanup plan

Material/Chemical	Storm Water Pollutants	Common Location*	Pollution Prevention Methods
Hydraulic oil/fluids	Mineral oil	Leaks or broken hoses from equipment	Spill prevention and cleanup plan
Gasoline	Benzene, ethyl benzene, toluene, xylene, MTBE	Secondary containment/staging area	Spill prevention and cleanup plan
Diesel Fuel	Petroleum distillate, oil & grease, naphthalene, xylenes	Secondary containment/staging area	Spill prevention and cleanup plan
Kerosene	Coal oil, petroleum distillates	Secondary containment/staging area	Spill prevention and cleanup plan
Antifreeze/coolant	Ethylene glycol, propylene glycol, heavy metals (copper, lead, zinc)	Leaks or broken hoses from equipment	Spill prevention and cleanup plan
Sanitary toilets	Bacteria, parasites, and viruses	Staging area	On-site portable toilet will be staked to ground, serviced regularly

*(Area where material/chemical is used on-site)

6. Spill Prevention and Response Plan

Describe who is responsible for containing and cleaning up spills. Provide a specific person's name and phone number. If a spill kit is located on site, add the location, if there is not a spill kit on site, please provide information on what to use (sand, etc) to contain spills.

Spill Plan:

All equipment and materials will be inspected daily by on-site supervisor (Gary Hill 435-503-2600). Supervisor will be made aware of any leaks or spills immediately. Spills will be isolated and prevented from spreading. Absorbent material will be placed over the spill and allowed to soak in, then the area will be over-excavated, and the material will be transported to the appropriate disposal location.

Any discharges in 24 hours equal to or in excess of the reportable quantities listed in 40 CFR 117, 40 CFR 110, and 40 CFR 302 will be reported to the National Response Center and the Division of Water Quality (DWQ) as soon as practical after knowledge of the spill is known to the permittee. The permittee shall submit within 14 calendar days of knowledge of the release a written description of: the release (including the type and estimate of the amount of material released), the date that such release occurred, the circumstances leading to the release, and measures taken and/or planned to be taken to the Division of Water Quality (DWQ), 288 North 1460 West, P.O. Box 144870, Salt Lake City, Utah 84114-4870. The Storm Water Pollution Prevention Plan must be modified within 14 calendar days of knowledge of the release to provide a description of the release, the circumstances leading to the release, and the date of the release. In addition, the plan must be reviewed to identify measures to prevent the reoccurrence of such releases and to respond to such releases, and the plan must be modified where appropriate.

Agency	Phone Number
National Response Center	(800) 424-8802
Division of Water Quality (DWQ) 24-Hr Reporting	(801) 538-6146; (801) 536-4123
Utah Department of Health Emergency Response	(801) 580-6681
Park City Fire Department	435-940-2500

Minimum spill quantities requiring reporting:

Material	Media Released To	Reportable Quantity
Engine oil, fuel, hydraulic & brake fluid	Land	25 gallons
Paints, solvents, thinners	Land	100 lbs (13 gallons)
Engine oil, fuel, hydraulic & brake fluid	Water	Visible Sheen
Refrigerant	Air	1 lb
Antifreeze, battery acid, gasoline, engine degreasers	Air, Land, Water	100 lbs (13 gallons)

Emphasis to:

- 1st Priority: Protect all people (including onsite staff)
- 2nd Priority: Protect equipment and property
- 3rd Priority: Protect the environment

1. Make sure the spill area is safe to enter and that it does not pose an immediate threat to health or safety of any person.
2. Check for hazards (flammable material, noxious fumes, cause of spill) – if flammable liquid, turn off engines and nearby electrical equipment. If serious hazards are present leave area and call 911. LARGE SPILLS ARE LIKELY TO PRESENT A HAZARD.
3. Stop the spill source and contain flowing spills immediately with spill kits, dirt or other material that will achieve containment.
4. Call co-workers and supervisor for assistance and to make them aware of the spill and potential dangers
5. If spilled material has entered a storm sewer, regardless of containment; contact the City Storm Water Division.
6. Cleanup all spills (flowing or non-flowing) immediately following containment. Clean up spilled material according to manufacturer specifications, for liquid spills use absorbent materials AND DO NOT FLUSH AREA WITH WATER.
7. Properly dispose of cleaning materials and used absorbent material according to manufacturer specifications.
8. Report the reportable quantity to the [Summit County](#) Storm Water Division.

Emergency Numbers

Utah Hazmat Response Officer 24 hrs	(801)-538-3745
Park City Police Department	435-615-5500
Summit County Engineering Division	(435)336-3250

7. SWPPP, Inspections and Corrective Action Reports

Inspection Schedule and Procedures: The permit requires inspections **once a week** (see permit Part 3). You must list and provide details of your BMPs in Appendix G. **Summit County requires all inspections be logged in ComplianceGo. Summit County will set up each contractor with an account in ComplianceGo, with an inspection report to fill out.**

Describe the general procedures for correcting problems when they are identified. Include responsible staff and time frames for making corrections:

Weekly inspections will be completed by Blayde McIntire of Altitude Engineering (307-679-8620). He will notify site supervisor Gary Hill of any necessary actions. Actions will be completed within 7 days or before any storm event.

Inspections and Corrective Actions: All inspections and corrective actions must be logged in ComplianceGo. Corrective Actions are automatically tracked on the site. Summit County will log corrective actions as “Action Items” and will appear red-flagged when you log on.

8. Training of Sub-Contractors

All sub-contractors, installers of utility connections, and others that perform activities that are affected by permit requirements will be informed about permit requirements that pertain to their scope of work.

Sub-Contractors are the Responsibility of the NOI holder. They shall be trained, and a record of that training should be kept on ComplianceGo

9. Changes to the SWPPP

All changes to this SWPPP must be redlined, dated, and initialed in the SWPPP document and on the site map. Modifications to the Site Map can be logged in ComplianceGo. Modifications to the SWPPP can also be made in the LOG on ComplianceGo.

10. Record Keeping

The following items should be kept at the project site available for inspectors to review:

1. A copy of the Common Plan Permit (A Link is provided in Appendix B)
2. The signed and certified NOI form (Appendix C, or on ComplianceGo)
3. Inspection reports (In ComplianceGo)

11. Delegation of Authority (if any)

Duly Authorized Representatives or Positions:

Company/Organization: Company of Representative.

Name: Authorized Representative Name.

Position: Representative Title.

Address: Click here to enter text.

City: Click here to enter text.

State: State

Zip: Zip Code

Telephone: (XXX) XXX-XXXX

Fax/Email: (XXX) XXX-XXXX

Owner/General Contractor Signature: _____ Date: _____

Additional Duly Authorized Representatives or Positions:

Company/Organization: Company of Representative.

Name: Authorized Representative Name.

Position: Representative Title.

Address: Click here to enter text.

City: Click here to enter text.

State: State

Zip: Zip Code

Telephone: (XXX) XXX-XXXX

Fax/Email: (XXX) XXX-XXXX

Owner/General Contractor Signature: _____ Date: _____

12. Discharge Information

Does your project/site discharge storm water into a Municipal Separate Storm Sewer System (MS4)?

Yes

No

Municipal Storm Drain System receiving the discharge from the construction project: **Summit County**

Receiving Waters (look up <http://mapserv.utah.gov/surfacewaterquality/> to identify your receiving water body). Examples of Receiving waters are "Silver Creek" "Weber River" "East Canyon Creek" "Bear River" "Yellow Creek"

Enter the name(s) of the first surface water(s) that receives storm water directly from your site and/or from the MS4 listed above. **Note:** multiple rows provided in the case that your site has more than one point of discharge in which each flows to different surface waters.

1. **Silver Creek**

2. Click here to enter name of receiving waters.

Impaired Waters (refer to <http://mapserv.utah.gov/surfacewaterquality/> in the left hand column to determine status of receiving water body). Examples of Impaired bodies of water are "Silver Creek" "East Canyon Creek" "Kimball Creek" "Echo Creek" "Chalk Creek"

Select any impaired surface water(s) that your site will discharge to, either directly or through the MS4 selected above.

Impaired Surface Water	Is this surface water impaired?	Pollutant(s) causing the impairment	Has a TMDL been completed?	Pollutant(s) for which there is a TMDL
Silver Creek	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	Use Class 1C: Cadmium, Nitrate as Total N, pH, Arsenic; Use Class 2B: pH; Use Class 3A: pH, Dissolved Oxygen, OE Bioassessment, Cadmium, Zinc; Use Class 4: Cadmium, pH, Total Dissolved Solids	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	Cadmium, Zinc
Click here to enter text.	<input type="checkbox"/> Yes <input type="checkbox"/> No	Click here to enter text.	<input type="checkbox"/> Yes <input type="checkbox"/> No	Click here to enter text.

13. Certification and Notification

I, Gary Hill, certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.



 Construction Operator:

This SWPPP should be signed and certified by the construction operator(s).

SWPPP Appendices

Ensure the following documentation is attached to the SWPPP:

Appendix A: SWPPP Site Maps

Appendix B: Common Plan Permit

Appendix C: Notice of Intent (NOI), and a copy of the NOT form unless you plan to terminate the permit on-line

Appendix D: Daily Site Check Log

Appendix G: BMP Specifications and Details (label BMPs to match the sections identified in this document.)


APPENDIX A: SWPPP Site Maps

Summit County will also add Maps into ComplianceGo.

Updates to Maps can easily be done on ComplianceGo.



SCALE: 1" = 20'
 0 10 20 40 60
 SCALE IN FEET

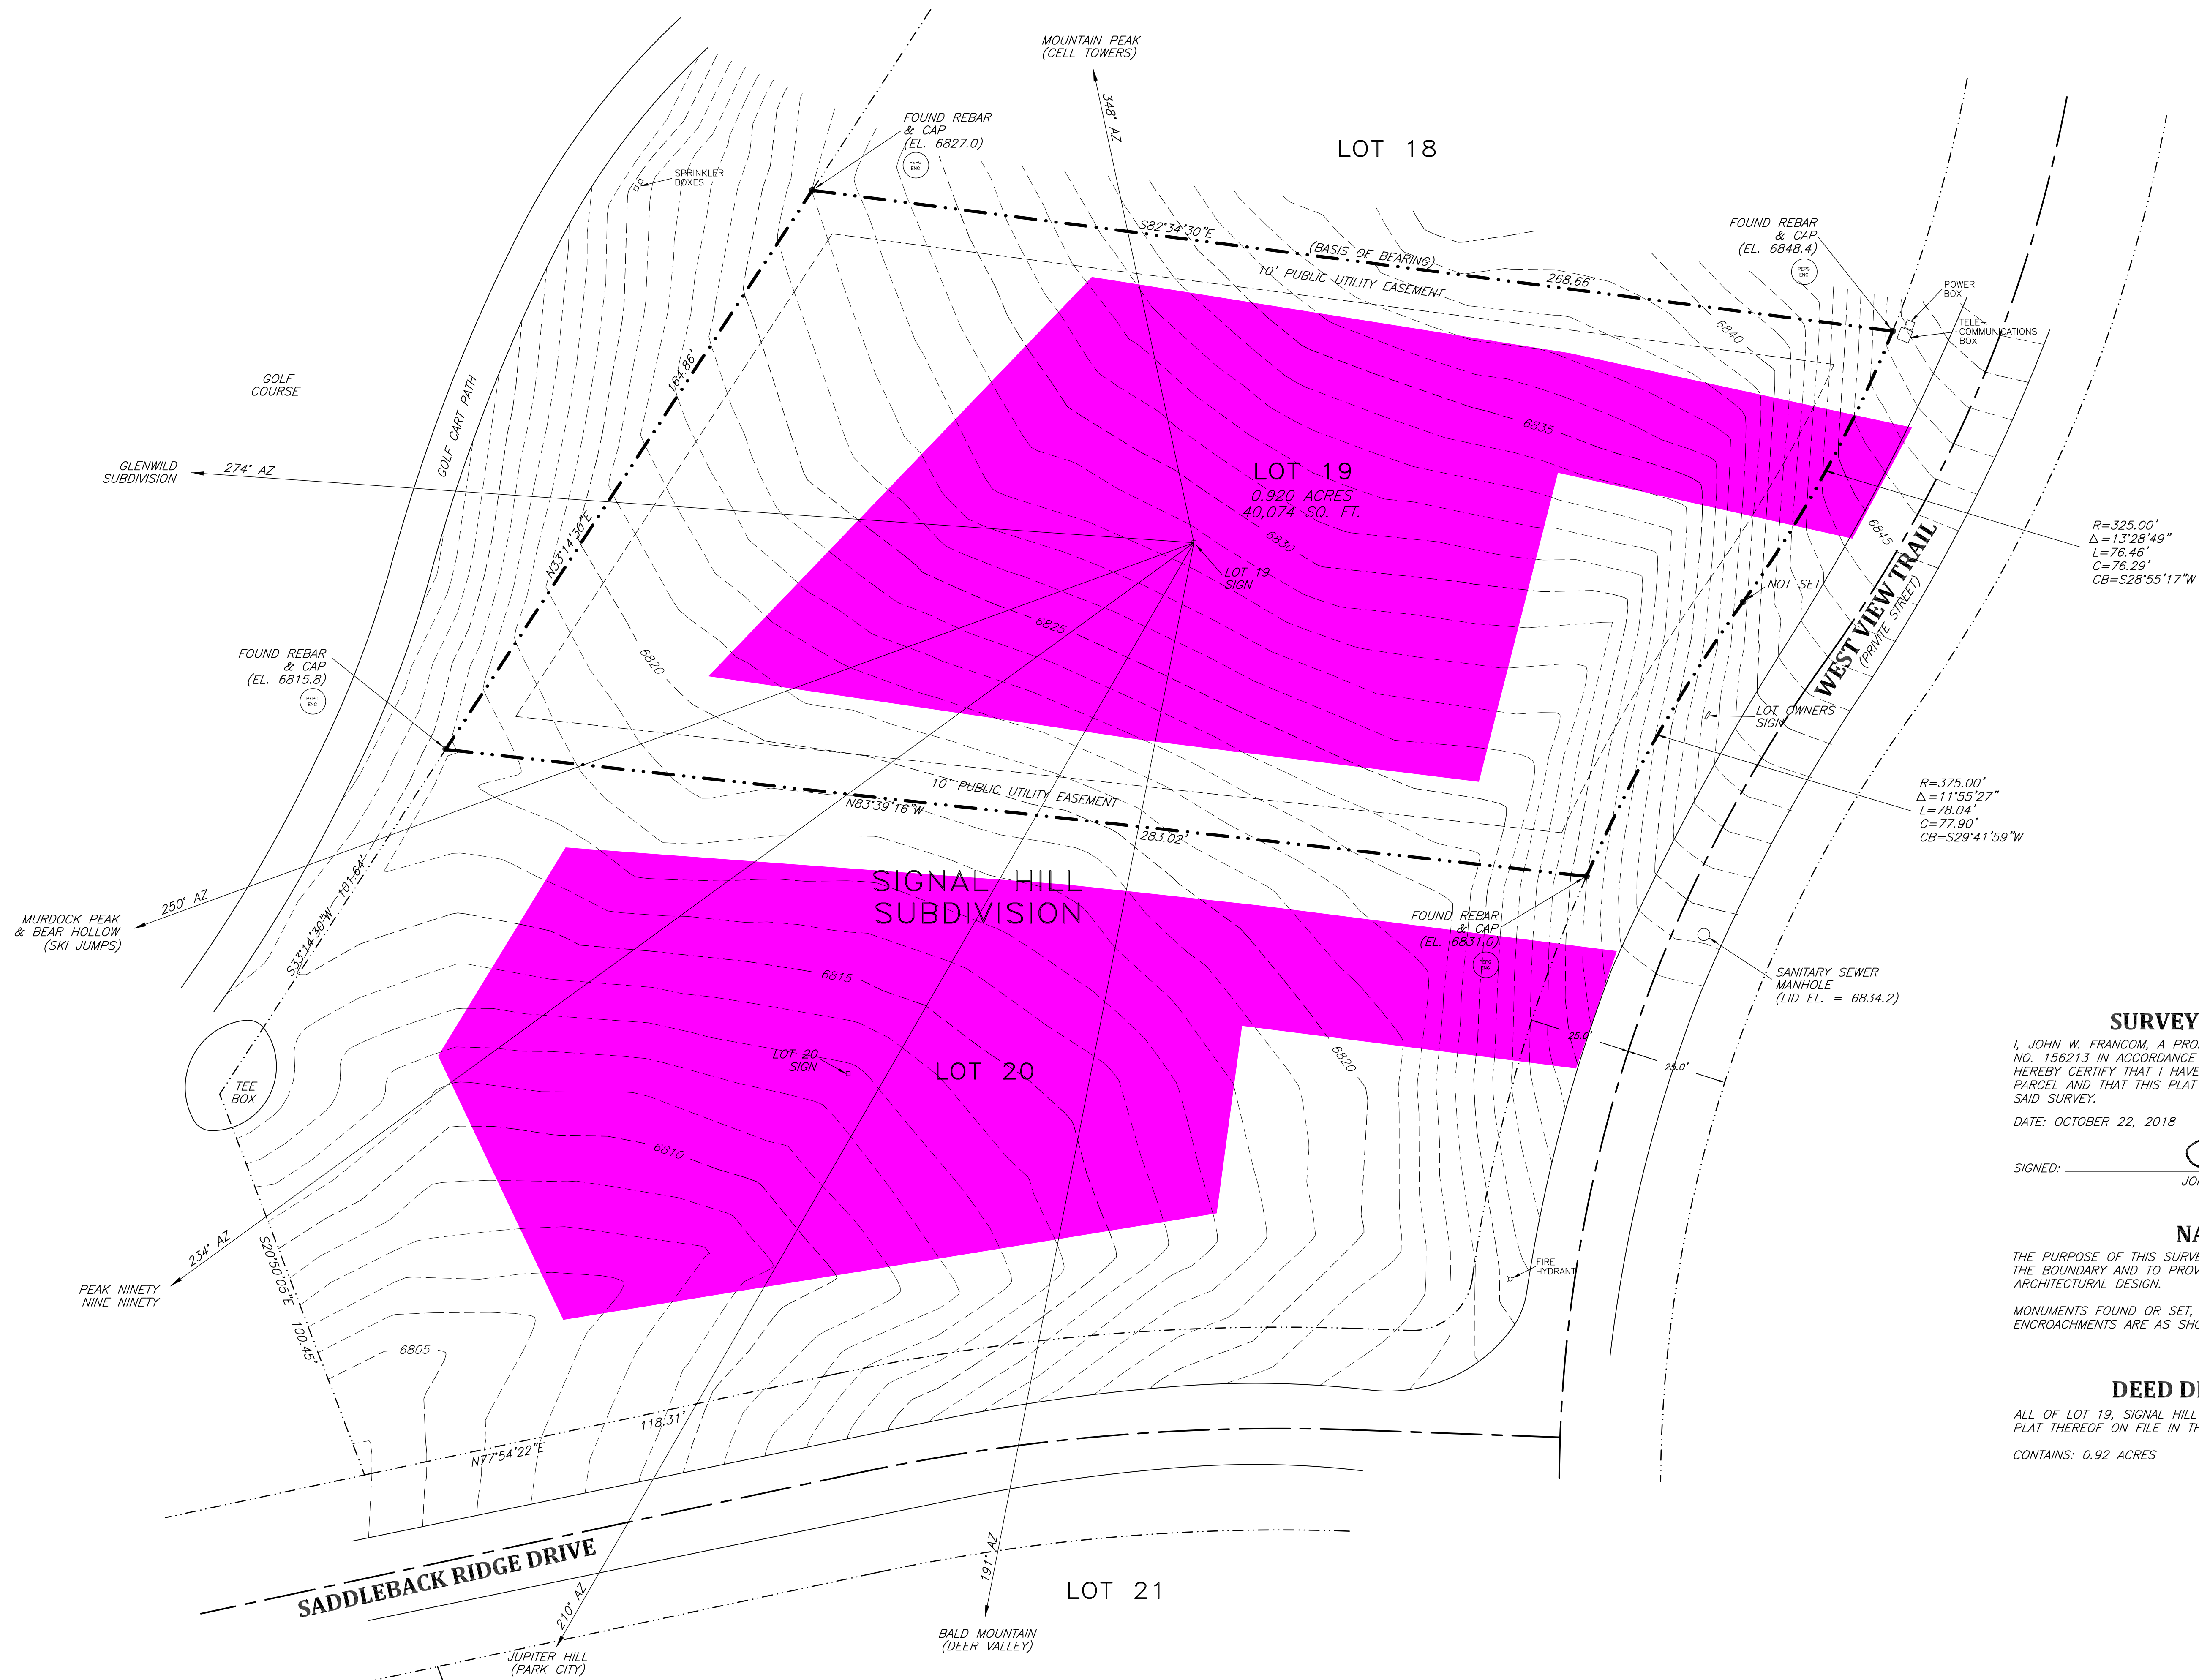

SURVEYOR'S CERTIFICATE

I, JOHN W. FRANCOM, A PROFESSIONAL LAND SURVEYOR HOLDING LICENSE NO. 156213 IN ACCORDANCE WITH THE LAWS OF THE STATE OF UTAH HEREBY CERTIFY THAT I HAVE MADE A SURVEY OF THE HEREON DESCRIBED PARCEL AND THAT THIS PLAT IS A TRUE AND CORRECT REPRESENTATION OF SAID SURVEY.

DATE: OCTOBER 22, 2018

SIGNED: 
 JOHN W. FRANCOM, P.L.S. 156213

NARRATIVE

THE PURPOSE OF THIS SURVEY IS TO RE-SURVEY AND FIELD STAKE THE BOUNDARY AND TO PROVIDE TOPOGRAPHIC INFORMATION PRIOR TO ARCHITECTURAL DESIGN.

MONUMENTS FOUND OR SET, THE BASIS OF BEARING AND ANY ENCROACHMENTS ARE AS SHOWN HEREON.

DEED DESCRIPTION


ALL OF LOT 19, SIGNAL HILL SUBDIVISION ACCORDING TO THE OFFICIAL PLAT THEREOF ON FILE IN THE SUMMIT COUNTY RECORDERS OFFICE. CONTAINS: 0.92 ACRES

EVANS LAND SURVEYING

BOUNDARY, TOPOGRAPHIC & CONSTRUCTION SURVEYS
 4568 HIGHLAND DRIVE, SUITE 110, SALT LAKE CITY, UTAH 84117

BUS.(801)272-3996

EMAIL: EVANSLANDSURVEYING@GMAIL.COM



GREG WALSKI

LOT 19, SIGNAL HILL
 3481 WEST VIEW TRAIL
 SUMMIT COUNTY, UTAH

LOCATED IN THE NORTHWEST QUARTER OF SECTION 13, TOWNSHIP 1 SOUTH, RANGE 4 EAST, SALT LAKE BASE & MERIDIAN

REVISIONS:

DRAWN BY: KUE
 CHECKED BY: JWF
 SURVEY DATE: 10/22/2018
 JOB NO: 18-126

SURVEYED BY: NJE/KUE
 CALCULATED BY: NJE
 ELEC. DATA COLLECTION
 DWG: GOWEST-19SH


SHEET DESCRIPTION

BOUNDARY & TOPOGRAPHIC SURVEY

SHEET NO.

1
 OF
ONE

INSPECTION	DESCRIPTION/REQUIREMENTS	CONTACT
DRIVEWAY / SITE STAKING	REQUIRED PRIOR TO ISSUANCE OF A BUILDING PERMIT. LOCATE / STAKE THE DRIVEWAY AT THE STREET AND AT THE ROAD RIGHT OF WAY / PROPERTY LINE AND LOCATE / STAKE ALL PROPERTY CORNERS WITH A 4 FOOT STEEL FENCE POST.	ENGINEERING
ROUGH GRADING	REQUIRED PRIOR TO SCHEDULING A FOOTING INSPECTION. SITE EROSION CONTROL MEASURES MUST BE INSTALLED AND DRIVEWAY MUST BE ROUGHLY GRADED ACCORDING TO PLAN.	ENGINEERING
FOOTING	SCHEDULE AFTER STEEL IS IN PLACE AND BEFORE CONCRETE IS POURED.	BUILDING
FOUNDATION	SCHEDULE AFTER STEEL IS IN PLACE IN THE FORMS AND BEFORE CONCRETE IS PLACED.	BUILDING
UNDER SLAB PLUMBING AND HEATING	BEFORE CONCRETE IS POURED OR PLUMBING HAS BEEN BACKFILLED.	BUILDING
CERTIFICATION OF ELEVATION AND/OR SURVEY	PERFORMED BY A LICENSED SURVEYOR. REQUIRED PRIOR TO SCHEDULING A FLOOR FRAMING INSPECTION. SEE REQUIREMENTS BELOW.	BUILDING
FLOOR FRAMING INSPECTION	REQUIRED PRIOR TO PLACING FLOOR SHEETING AND INCLUDES FOOTING DRAIN INSPECTION.	BUILDING
SHEAR WALL	AFTER THE BUILDING IS UP TO THE SQUARE AND ALL SHEAR WALLS HAVE BEEN NAILLED AND ALL THE TIE DOWNS AND SHEAR WALL CONNECTIONS HAVE BEEN INSTALLED.	BUILDING
FIRE SPRINKLERS	REQUIRED PRIOR TO FOUR-WAY INSPECTION, WHEN REQUIRED BY THE LOCAL FIRE DISTRICT.	BUILDING
FOUR-WAY	THIS INSPECTION IS PERFORMED AFTER ALL ROUGH ELECTRICAL, PLUMBING, AND MECHANICAL HAVE BEEN INSTALLED. ALL FRAMING IS COMPLETE. SHEAR WALLS PREVIOUSLY INSPECTED, AND TRUSS SPECIFICATIONS ARE ON THE JOB FOR THE INSPECTOR TO READ. PLUMBING SHALL HAVE EITHER AN AIR OR WATER PRESSURE TEST ON THEM WHEN THE INSPECTOR ARRIVES.	BUILDING
WEATHER BARRIER / STUCCO LATH	WEATHER BARRIER SHALL BE INSPECTED PRIOR TO APPLYING VENEER. APPROVED STUCCO I.C.G. RESEARCH REPORTS ON SITE.	BUILDING
GAS METER SET	REQUIRED BEFORE GAS METER CLEARANCE IS GIVEN TO DOMINION ENERGY.	BUILDING
MASONRY WALL / BOND BEAM	STEEL IN MASONRY AND BEFORE CONCRETE/GROUT IS POURED.	BUILDING
INSULATION	PRE-SHEETROCK INSULATION CERTIFICATE REQUIRED.	BUILDING
DRYWALL NAILING	THIS IS TO BE DONE BEFORE DRYWALL IS TAPED.	BUILDING
POWER TO PANEL	BUILDING MUST BE UP WITH PERMANENT ROOF INSTALLED.	BUILDING
DRIVEWAY PRE-SURFACING	SITE EROSION CONTROL MEASURES MUST BE INSTALLED AND DRIVEWAY GRADED TO ITS FINAL CONFIGURATION.	ENGINEERING
FINAL DRIVEWAY AND SITE INSPECTION	REQUIRED PRIOR TO CERTIFICATE OF OCCUPANCY AND/OR BOND RELEASE. DRIVEWAY MUST BE SURFACED AND SITE MUST BE RE-VEGETATED (INSPECTIONS MAY BE SCHEDULED SEPARATELY).	ENGINEERING
FLOOD PLAN ELEVATION CERTIFICATE	FEMA ELEVATION CERTIFICATE (IF APPLICABLE) REQUIRED PRIOR TO CERTIFICATE OF OCCUPANCY. FORM MUST BE FILED WITH FEMA AND A COPY PROVIDED TO THE ENGINEERING DEPARTMENT.	ENGINEERING
FINAL	ALL WORK IS DONE AND BUILDING COMPLETE.	BUILDING
CERTIFICATE OF OCCUPANCY	REQUIRED PRIOR TO ANYONE OCCUPYING THE STRUCTURE. A CERTIFICATE OF OCCUPANCY WILL BE ISSUED ONCE THE FINAL CLEARANCES HAVE BEEN OBTAINED BY THE BUILDER AND BROUGHT TO THE BUILDING DEPARTMENT'S OFFICE IN COALVILLE. 1) SNYDERVILLE BASIN RESIDENTIAL: FINAL FROM BUILDING DEPARTMENT, FINAL FROM ENGINEERING DEPARTMENT, FINAL LETTER FROM SNYDERVILLE BASIN WATER RECLAMATION DISTRICT, FINAL WATER CONCURRENCY LETTER FROM APPROPRIATE WATER COMPANY, FINAL FROM PARK CITY FIRE DISTRICT (IN REQUIRED SUBDIVISIONS). 2) EASTERN SUMMIT COUNTY: FINAL FROM BUILDING DEPARTMENT, FINAL FROM ENGINEERING DEPARTMENT, FINAL FROM FIRE DISTRICT AND FINAL FROM HEALTH DEPARTMENT.	BUILDING


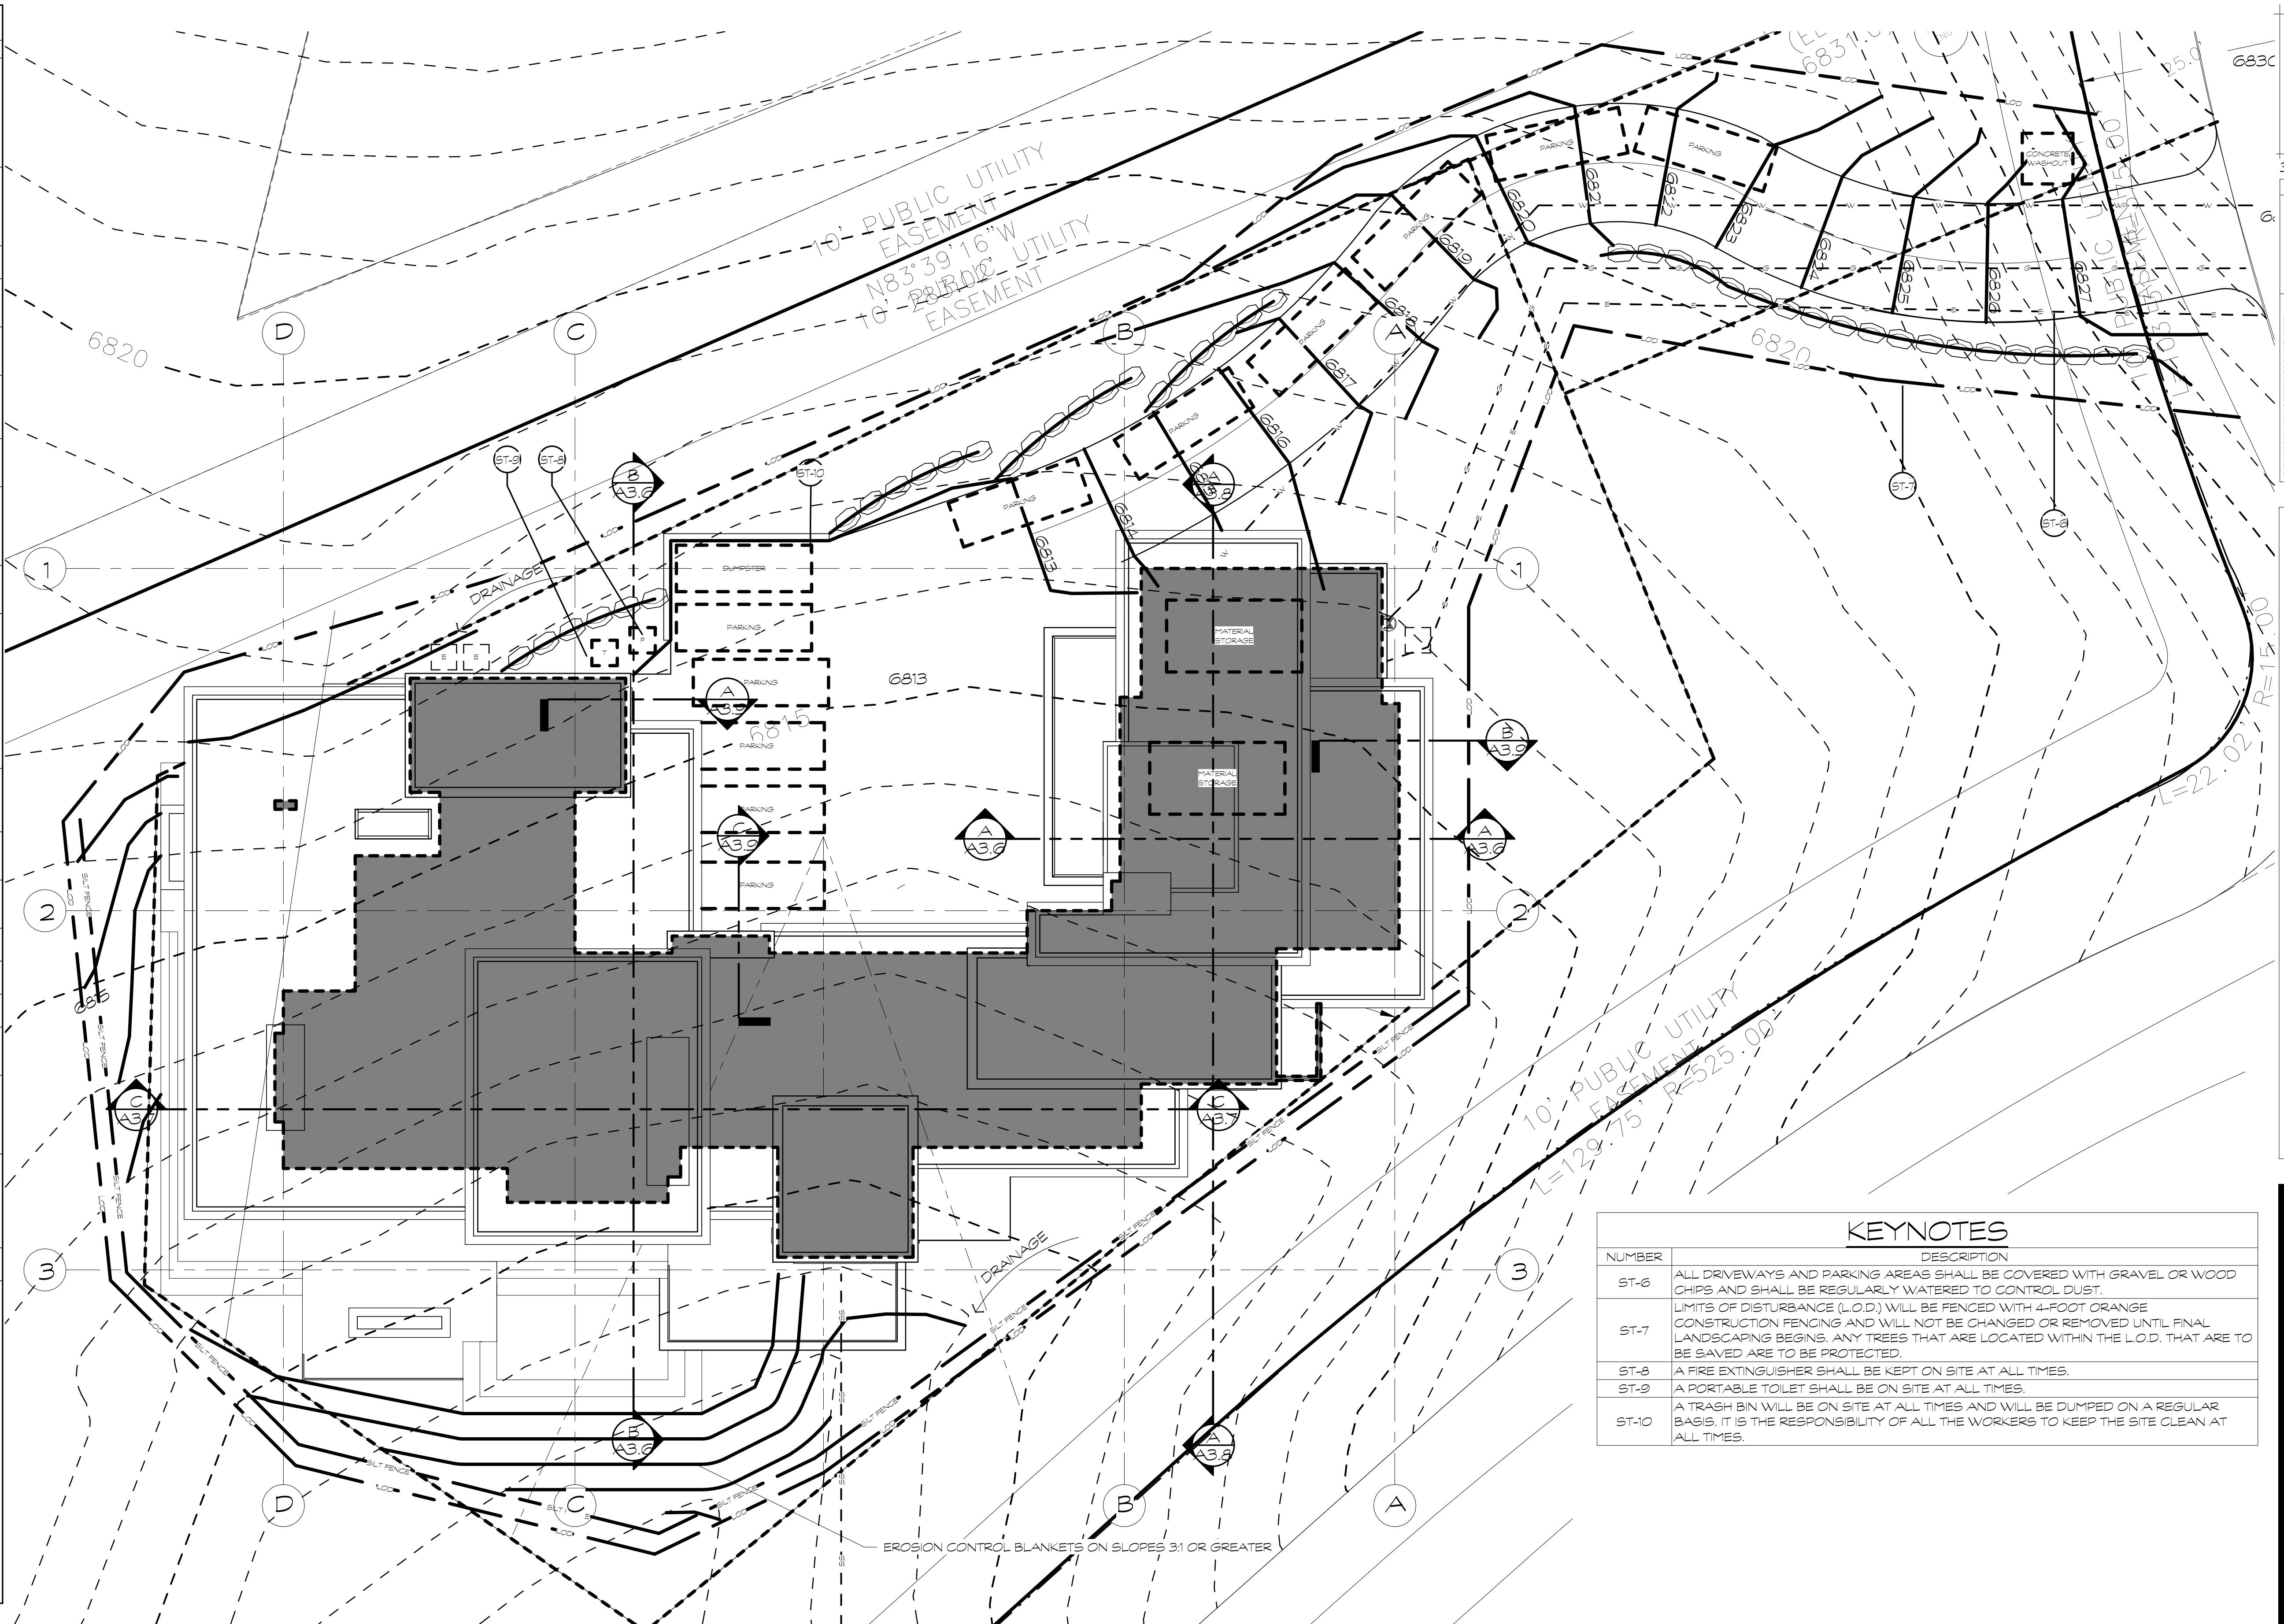


SITE GENERAL NOTES	
1	CONTRACTOR TO FIELD VERIFY LOCATION OF UTILITY LINES AS REQUIRED.
2	CONTRACTOR TO FIELD VERIFY MIN. 3'-0" SEPARATION BETWEEN GAS AND ELECTRICAL LINES.
3	REESTABLISH NATURAL GRADE AND NATURAL VEGETATION. PROVIDE TEMP. IRRIGATION TO ASSURE ESTABLISHED VEGETATION.
4	SURFACE WATER SHALL DRAIN AWAY FROM THE HOUSE AT ALL POINTS. DIRECT THE DRAINAGE WATER TO THE STREET OR TO AN APPROVED DRAINAGE COURSE, BUT NOT ONTO NEIGHBORING PROPERTIES. THE GRADE SHALL FALL A MINIMUM OF 6 INCHES WITHIN THE FIRST 10 FT. (RC R401.3)
5	RETAINING WALLS (4' OR SUPPORTING A SURCHARGE), SWIMMING POOLS, SOLAR AND/OR GEO-THERMAL HEATING SYSTEMS, AND PHOTO-VOLTAIC AND/OR WIND-GENERATED ELECTRICAL SYSTEMS REQUIRE SEPARATE PERMITS. SEPARATE PLANS, SPECIFICATIONS AND APPLICATIONS ARE TO BE SUBMITTED AND REVIEWED PRIOR TO ISSUANCE OF THESE PERMITS.

KEYNOTES	
NUMBER	DESCRIPTION
ST-6	ALL DRIVEWAYS AND PARKING AREAS SHALL BE COVERED WITH GRAVEL OR WOOD CHIPS AND SHALL BE REGULARLY WATERED TO CONTROL DUST. LIMITS OF DISTURBANCE (L.O.D.) WILL BE FENCED WITH 4-FOOT ORANGE CONSTRUCTION FENCING AND WILL NOT BE CHANGED OR REMOVED UNTIL FINAL LANDSCAPING BEGINS. ANY TREES THAT ARE LOCATED WITHIN THE L.O.D. THAT ARE TO BE SAVED ARE TO BE PROTECTED.
ST-8	A FIRE EXTINGUISHER SHALL BE KEPT ON SITE AT ALL TIMES.
ST-9	A PORTABLE TOILET SHALL BE ON SITE AT ALL TIMES.
ST-10	A TRASH BIN WILL BE ON SITE AT ALL TIMES AND WILL BE DUMPED ON A REGULAR BASIS. IT IS THE RESPONSIBILITY OF ALL THE WORKERS TO KEEP THE SITE CLEAN AT ALL TIMES.

CONSTRUCTION MITIGATION PLAN

SCALE: 1" = 10'-0"

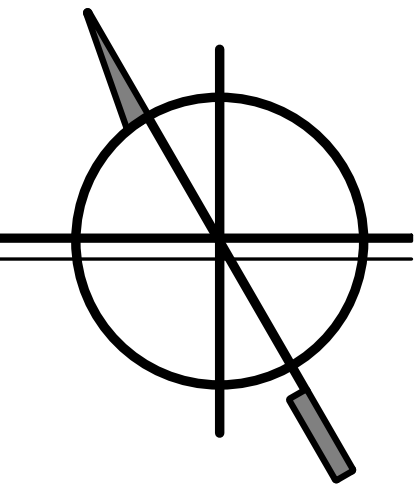

30 DECEMBER 2020
REVISIONS

A NEW DESIGN FOR THE:
SOBEY RESIDENCE
3457 E WESTVIEW TRL.
PARK CITY, UTAH 84098
LOT 20
SIGNAL HILL




UP WALL DESIGN
1930 S. 1100 E. S.L.C. UT 84106 (801) 485-0708

A1.4
CONSTRUCTION MITIGATION PLAN

THESE DRAWINGS AND SPECIFICATIONS ARE THE PROPERTY OF UTAH PROJECTS LOGO DESIGN, INC. AND ARE NOT TO BE REPRODUCED OR TRANSMITTED IN ANY FORM OR BY ANY MEANS, ELECTRONIC OR MECHANICAL, INCLUDING PHOTOCOPYING, RECORDING, OR BY ANY INFORMATION STORAGE AND RETRIEVAL SYSTEM, WITHOUT THE WRITTEN PERMISSION OF UTAH PROJECTS LOGO DESIGN, INC. ANY UNAUTHORIZED REPRODUCTION OR TRANSMISSION OF THESE DRAWINGS AND SPECIFICATIONS IS STRICTLY PROHIBITED. UTAH PROJECTS LOGO DESIGN, INC. IS NOT RESPONSIBLE FOR ANY ERRORS OR OMISSIONS IN THESE DRAWINGS AND SPECIFICATIONS. THE USER ASSUMES ALL LIABILITY FOR THE USE OF THESE DRAWINGS AND SPECIFICATIONS. UTAH PROJECTS LOGO DESIGN, INC. IS NOT RESPONSIBLE FOR ANY DAMAGE TO PROPERTY OR PERSONS ARISING FROM THE USE OF THESE DRAWINGS AND SPECIFICATIONS. UTAH PROJECTS LOGO DESIGN, INC. IS NOT RESPONSIBLE FOR ANY CONSTRUCTION DEFECTS OR OMISSIONS. UTAH PROJECTS LOGO DESIGN, INC. IS NOT RESPONSIBLE FOR ANY DELAYS OR INTERRUPTIONS IN THE CONSTRUCTION PROCESS. UTAH PROJECTS LOGO DESIGN, INC. IS NOT RESPONSIBLE FOR ANY COST OVERRUNS OR UNDER-RUNS. UTAH PROJECTS LOGO DESIGN, INC. IS NOT RESPONSIBLE FOR ANY CHANGES TO THE DRAWINGS AND SPECIFICATIONS. UTAH PROJECTS LOGO DESIGN, INC. IS NOT RESPONSIBLE FOR ANY DISPUTES OR LITIGATION. UTAH PROJECTS LOGO DESIGN, INC. IS NOT RESPONSIBLE FOR ANY INJURY OR DEATH. UTAH PROJECTS LOGO DESIGN, INC. IS NOT RESPONSIBLE FOR ANY OTHER DAMAGES. UTAH PROJECTS LOGO DESIGN, INC. IS NOT RESPONSIBLE FOR ANY OTHER LIABILITY.

A NEW DESIGN FOR THE :
SOBEY RESIDENCE
3457 E WESTVIEW TRL.
PARK CITY, UTAH 84098
LOT 20
SIGNAL HILL




UP WALL
DESIGN
1930 S. 1100 E. S.L.C. UT 84106
(801) 485-0708

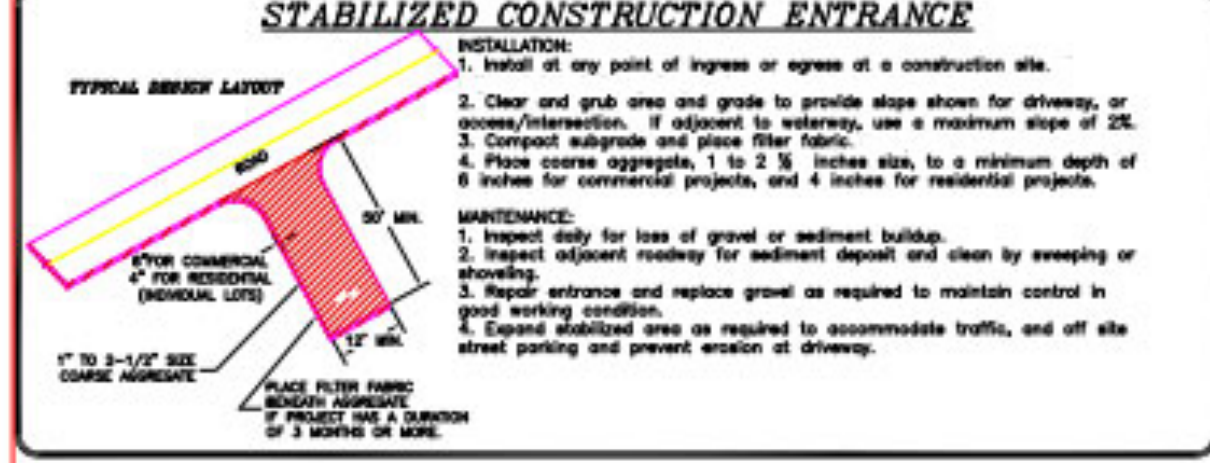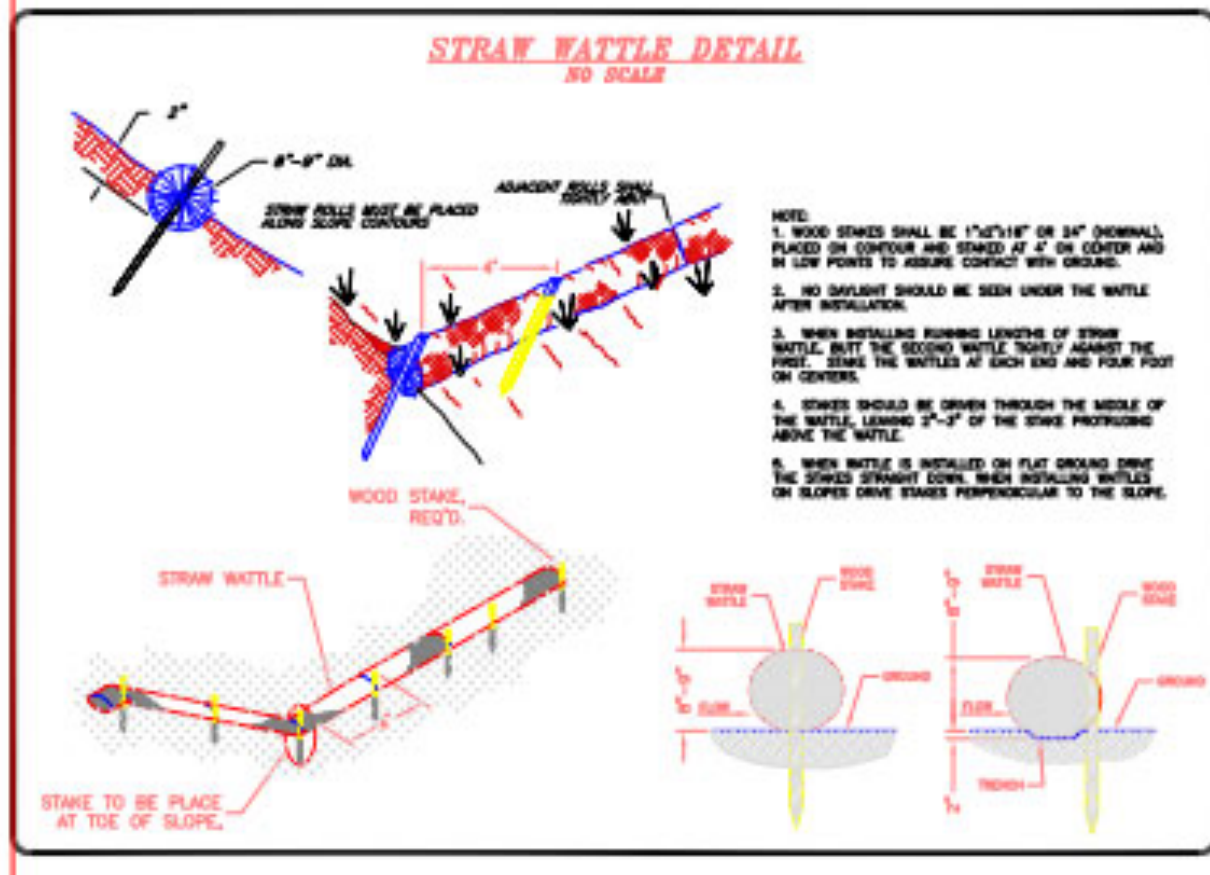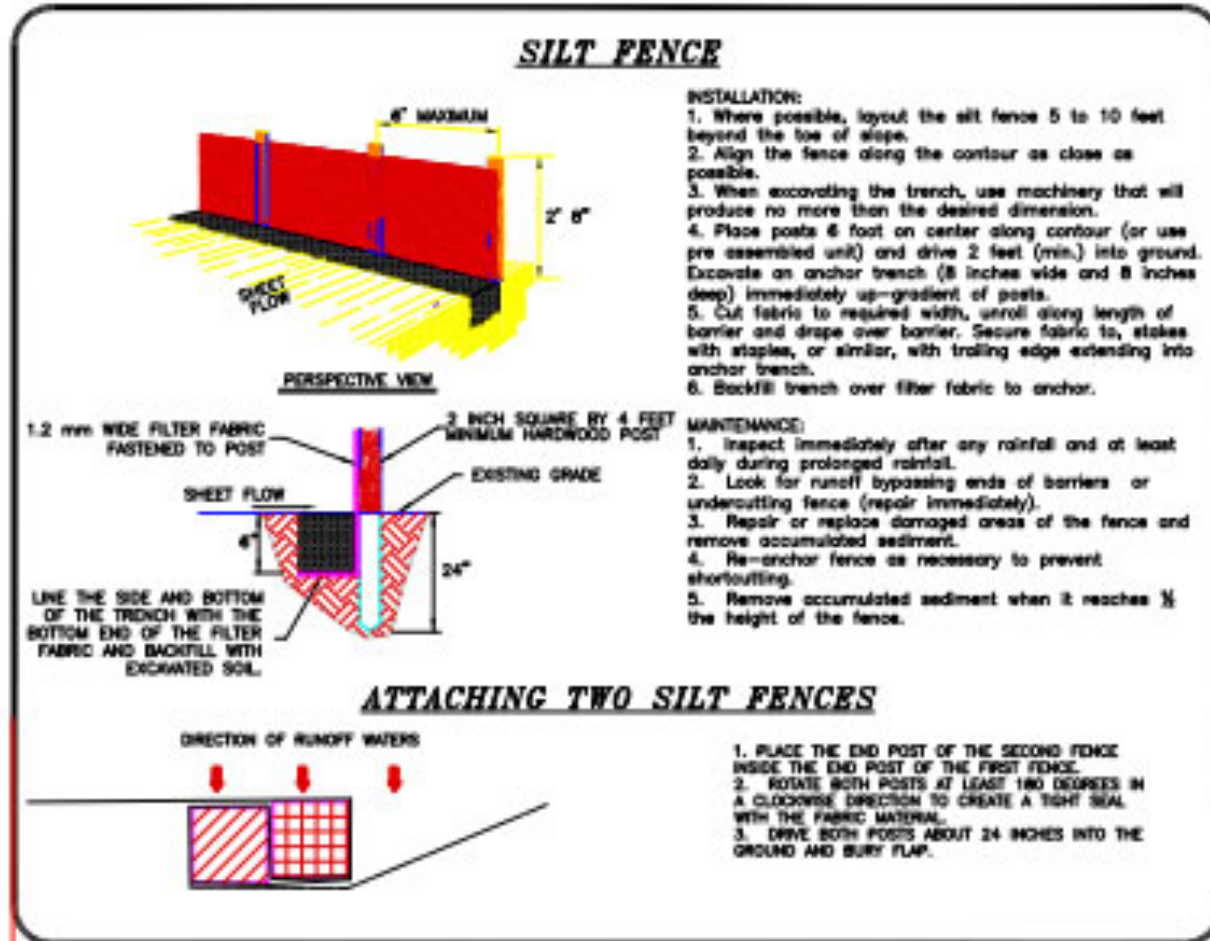

Required Inspections Table

Inspection	Description/Requirements	Contact
Driveway/ Site Staking	Required prior to issuance of a Building Permit. Locate stake the driveway at the street and at the road right of way/property line and locate/stake all property corners.	Engineering
Rough Grading	Required prior to scheduling a Final Inspection. Site Erosion Control measures must be installed and driveway must be roughly graded according to Plan.	Engineering
Footings	Schedule after steel is in place and before the concrete is poured.	Building
Foundations	Schedule after steel is in place in the forms and before concrete is placed.	Building
Under Slab Plumbing & Heating	Before concrete is poured or plumbing has been backfilled.	Building
Certificate of Erection and/or Firearm Inspection	Performed by a licensed surveyor. Required prior to scheduling a Floor Surface Inspection. See my comments below.	Building
Floor Framing Inspection	Required prior to placing floor sheathing and includes footing. Draw inspection.	Building
Shear Wall	After the building is up to "the square" and all shear walls have been sited and all tie downs and shear wall connections have been installed.	Building
Fire Sprinklers	Required prior to leak water inspection, when required by the local Fire District.	Building
Four Way	This inspection is performed after all rough electrical, plumbing, and mechanical has been installed. All framing is complete, shear walls previously inspected, and most specifications are on the job for the inspector to read. Flashing shall have either air or water pressure test as then when the inspector arrives.	Building
Weather Barrier/Window Lath	Weather barrier shall be inspected prior to applying window. Appointed check I.C.C. inspector reports on site.	Building
Gas Meter Set	Required before gas meter clearance is given to Gasmaster.	Building
Masonry and/wood beam	Steel in masonry and before concrete/pour is placed.	Building
Insulation	Pro-Shotrock, insulation certificate required.	Building
Driveway Nailing	This is done before gravel is laid.	Building
Proven to Pass	Building must be up with permanent roof installed.	Building
Driveway pre-surfacing	Site Erosion Control measures must be installed and driveway graded to it's final configuration.	Engineering
Final Driveway and Site Inspection	Required prior to Certificate of Occupancy and/or Road Release. Driveway must be surfaced and site must be re-vegetated (inspections may be scheduled separately). If the site is not re-vegetated, the erosion control measures must be in place and installed correctly.	Engineering
Flood Plain Elevation Certificate	FEMA Elevation Certificate (if applicable) required prior to Certificate of Occupancy. Forms must be filed with FEMA and a copy provided to the Engineering Department.	Engineering
Final	All work is DONE and building complete. Final clearances from the waste water district for sewer, County Health Department for septic, and fire district for sprinkler systems must be on the project for this inspection. Required for Certificate of Occupancy.	Building
Certificate of Occupancy	Required prior to anyone occupying the structure. A Certificate of Occupancy will be issued once the final clearances have been obtained by the holder and brought to the Building Department's office in Cash-ite. 1) Snowville Basin Residential: Final from Building Department, Final from Engineering Department, Final from Basin Water Reclamation District, Final water conveyance letter from appropriate water company, Final from Park City Fire District (in reps and subdivisions). 2) Eastern Summit County: Final from Building Department, Final from Engineering Department, Final from Fire District and Final from Health Department.	Building
ECP Road Release Inspection	Required to verify that the site has been fully stabilized (re-vegetated). Inspection is required prior to applicant receiving a release of their Erosion Control Bond. Applicant must provide a written record for the release of the bond.	Engineering


- ### Construction Mitigation Plan Notes
- Show location for dumpster, portable toilets, materials storage, parking
 - Construction parking traffic may not block the street without a permit (available from the Engineering Division)
 - Mud trucked out onto the street must be cleaned prior to the end of the work day
 - The construction site must be maintained in a neat manner. Trash and other debris may not accumulate outside the dumpster.
 - Roadside parking is not allowed from November 1st to April 1st
- Concrete washout areas may be prefabricated concrete washout containers, or self-installed structures (above-grade or below-grade).
- Prefabricated containers are most resistant to damage and protect against spills and leaks. Companies may offer delivery service and provide regular maintenance and disposal of solid and liquid waste.
 - If self-installed concrete washout areas are used, below-grade structures are preferred over above-grade structures because they are less prone to spills and leaks.
 - Self-installed above-grade structures should only be used if excavation is not practical.

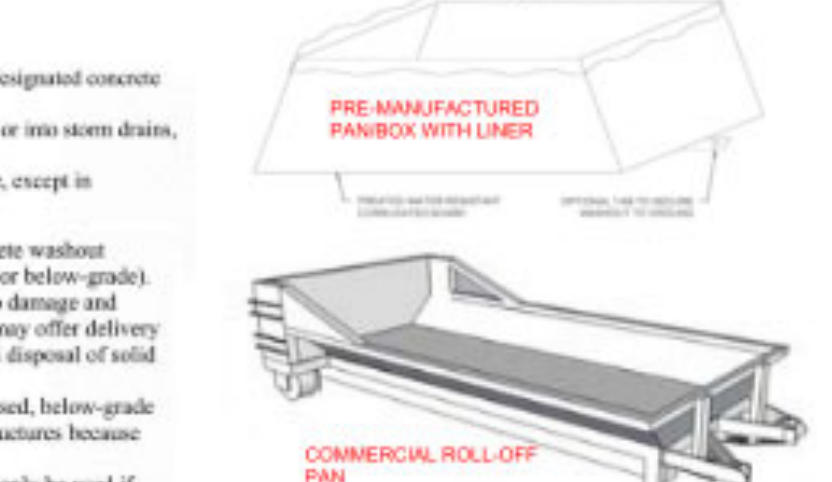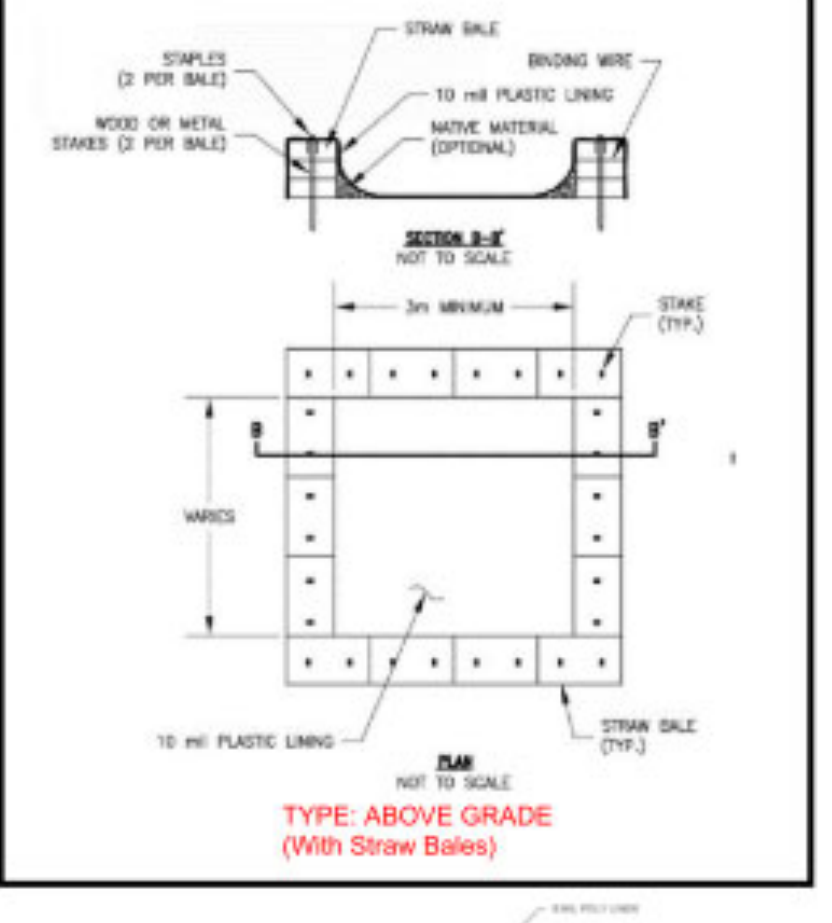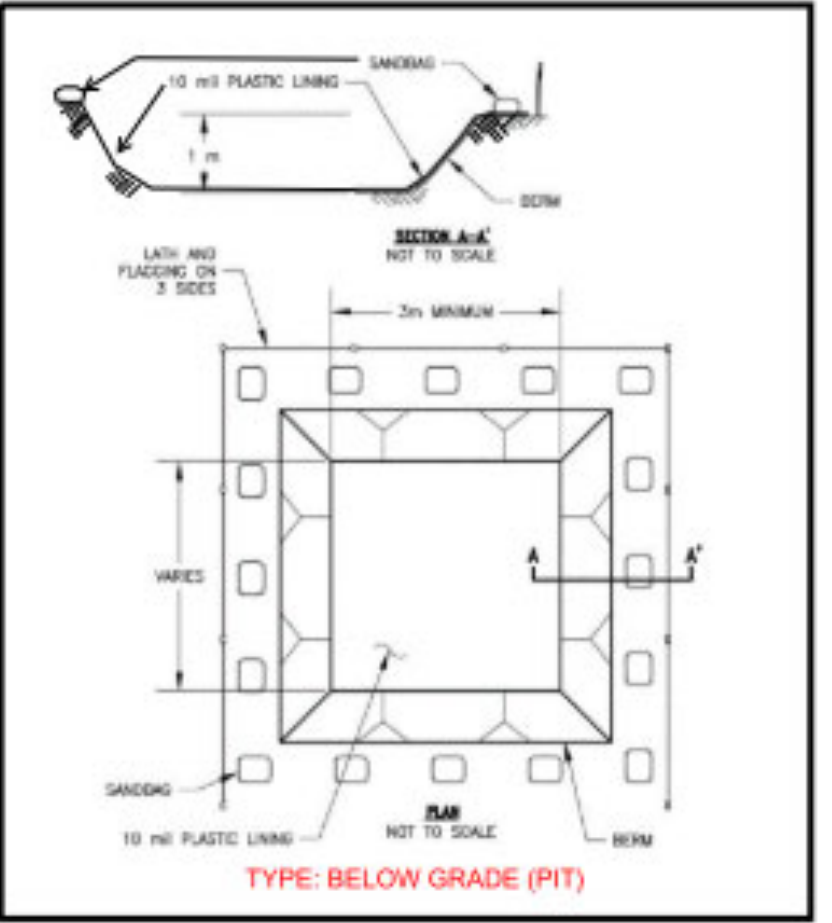

Summit County, Utah
Department of Public Works
Division of Engineering

Summit County, Utah
Standard Drawing
Residential Erosion Control Plan

SHEET NO:
SC-1

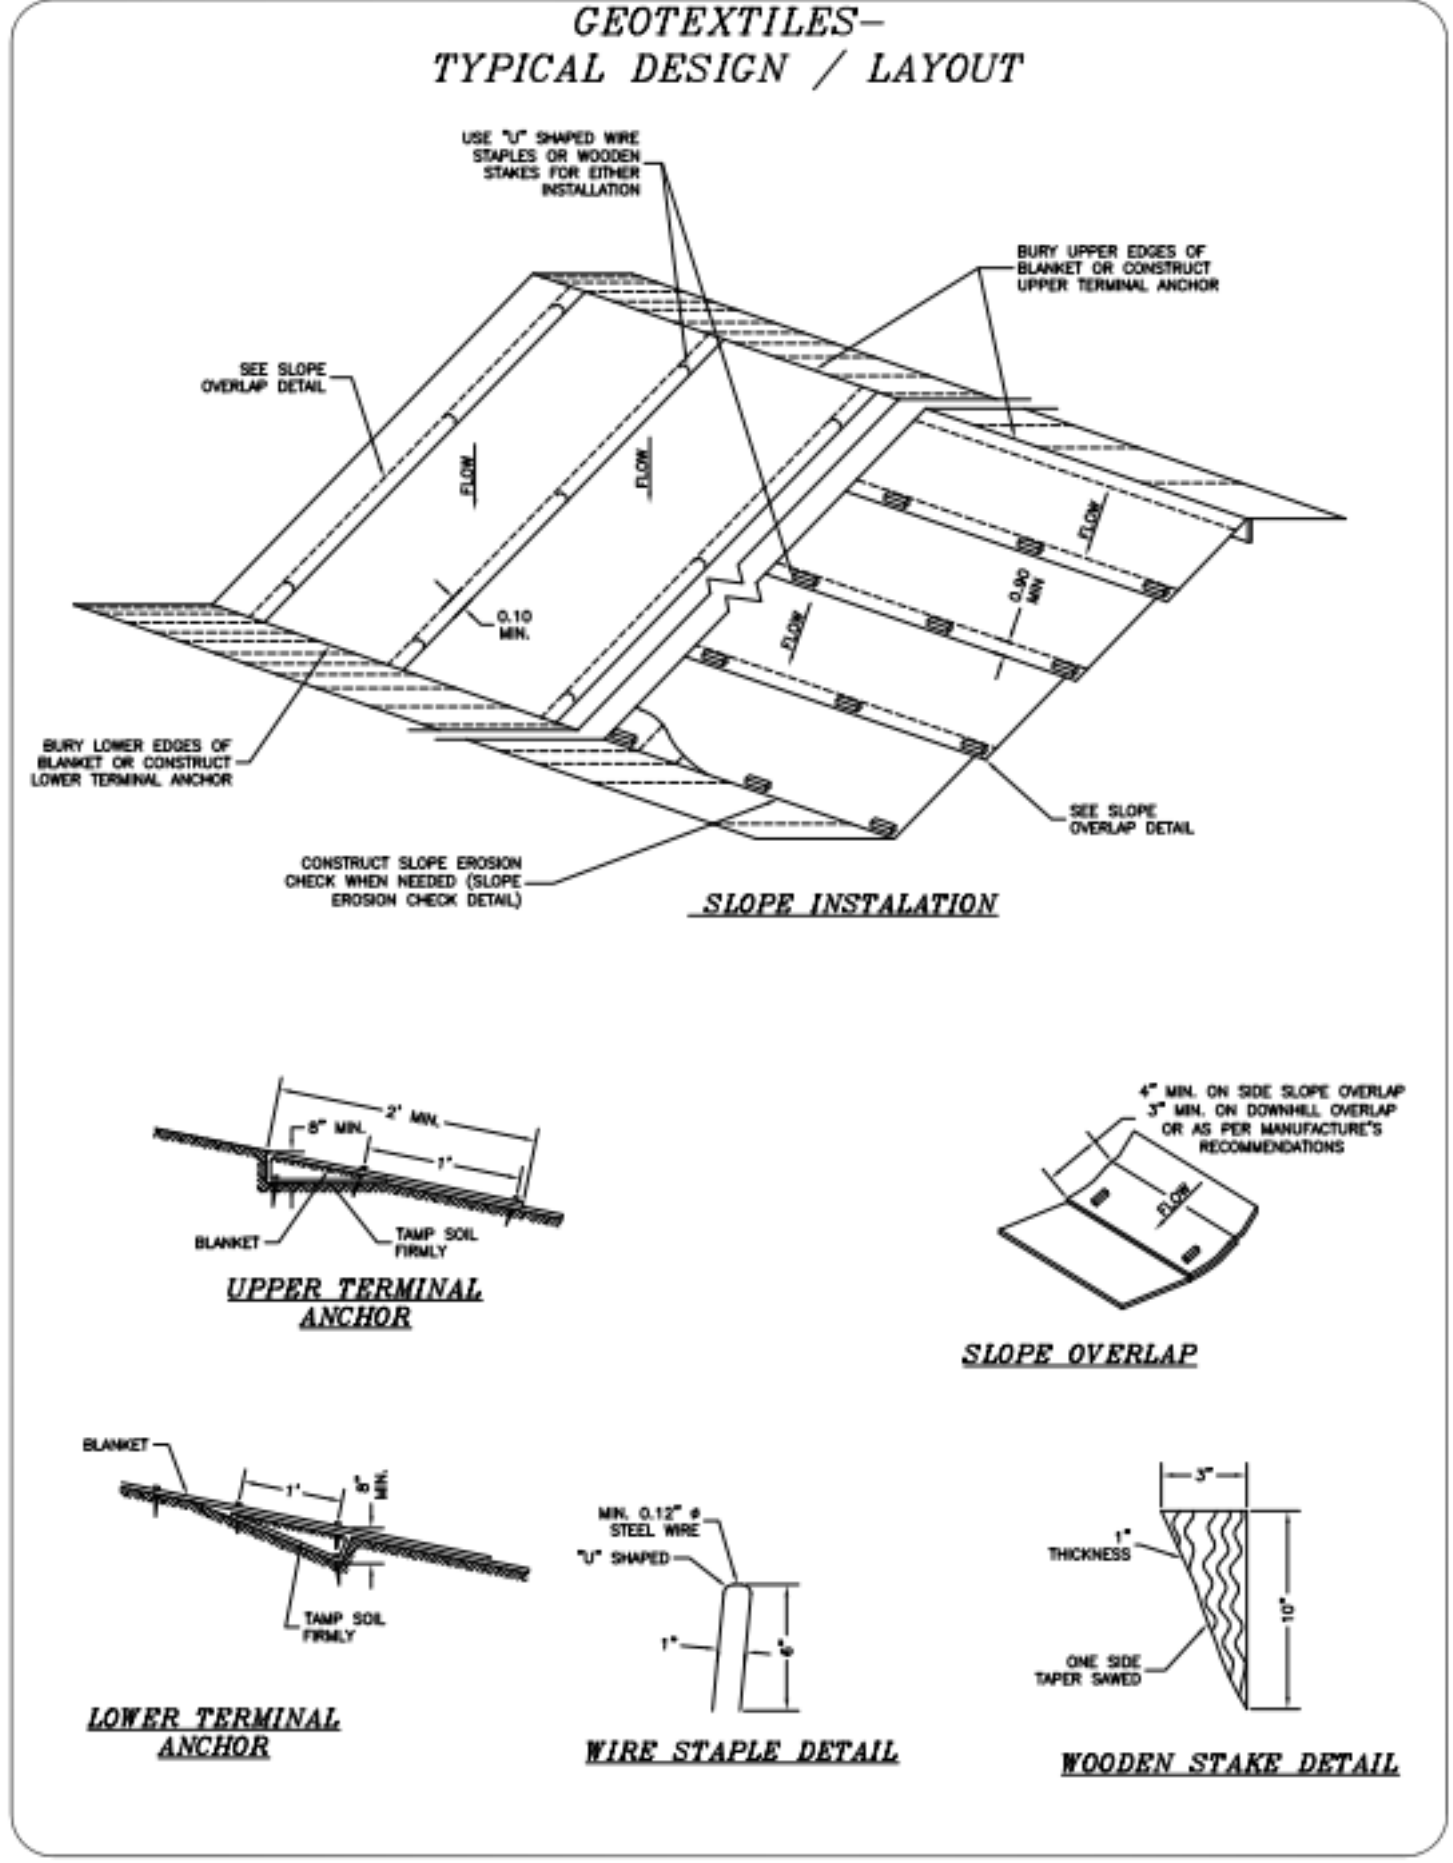

APPENDIX B: Common Plan Permit

Find the permit on <https://deq.utah.gov/water-quality/general-construction-storm-water-updes-permits>

APPENDIX C: Notice of Intent and Termination.

Find the Notice of Termination Form at <https://deq.utah.gov/water-quality/general-construction-storm-water-updes-permits>

However, termination of the project can be done on-line at <https://secure.utah.gov/stormwater>

(You must log in using the same username that you applied for your NOI with. If you completed a paper NOI you must complete a paper NOT.)



Notice of Intent (NOI) for Storm Water Discharges Associated with Construction
Activity Under the Common Plan Permit (CPP) UPDES General Permit
No. UTRH00000

NOI

Permit Information

Master Permit Number: UTRH00000

UPDES ID: UTRH02849

State/Territory to which your project/site is discharging: UT

Is your project/site located on federally recognized Indian Country Lands? No

Which type of form would you like to submit? Notice of Intent (NOI)

Have stormwater discharges from your project/site been covered previously under an UPDES permit? No

Has a Stormwater Pollution Prevention Plan (SWPPP) been prepared in advance of filling this NOI, as required? Yes

Owner/Operator Information

Owner Information

Owner: Midway Construction Company

Status of Owner: Private

Owner Mailing Address:

Address Line 1: PO Box 490

Address Line 2:

City: Heber City

ZIP/Postal Code: 84032

State: UT

Owner Point of Contact Information

First Name Middle Initial Last Name: Gary . Hill

Title: Site Supervisor and Owner

Phone: 435-503-2600

Ext.:

Email: gary@mcchomes.com

Operator Information

Is the Operator Information the same as the Owner Information? Yes

NOI Preparer Information

This NOI is being prepared by someone other than the certifier.

First Name Middle Initial Last Name: Blayde . McIntire

Organization: Altitude Engineering

Phone: 307-679-8620

Ext.:

Email: blayde.mcintire@gmail.com

Project/Site Information

Project/Site Name: Sobey Residence

Project Number:

Project/Site Address

Address Line 1: 3457 E Westview Trail

Address Line 2:

City: Park City

ZIP/Postal Code: 84098

State: UT

County or Similar Division: Summit

Have you submitted a Fugitive Dust Control Plan to UT Division of Air Quality? No

Latitude/Longitude for the Project/Site

Coordinate System: Decimal Degrees

Latitude/Longitude: 40.738°N, 111.449°W

Estimated Project Start Date: 06/01/2021

Estimated Project End Date: 11/01/2022

Total Area of Plot (in Acres): 0.97

Estimated Area to be Disturbed (in Acres): 0.5

Proposed Best Management Practices

Silt Fence/Straw Wattle/Perimeter Controls

Seeding/Preservation of Vegetation

Proposed Good Housekeeping Practices

Sanitary/Portable Toilet

Washout Areas

Garbage/Waste Disposal

Track Out Controls

Spill Control Measures

Site Activity Information

Municipal Separate Storm Sewer System (MS4) Operator Name: Summit County (Unincorporated Areas)

Receiving Water Body: Silver Creek

This is known

What is the estimated distance to the nearest water body? 1.39

Unit: Miles

Is the receiving water designated as impaired? Yes

Does this project site have any other UPDES permits? No

Certification Information

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I have no personal knowledge that the information submitted is other than true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations. Signing an electronic document on behalf of another person is subject to criminal, civil, administrative, or other lawful action.

Certified By: Gary C. Hill

Certifier Title: Project Manager

Certifier Email: gary@mcchomes.com

Certified On: 04/19/2021 12:57 PM ET

APPENDIX D: Daily Self-Inspection Log (permit part 3.2.2).

Certified

under the direction of
The Utah Chapter of the American Public Works Association
and the
Utah Storm Water Committee
in coordination with the
State of Utah Department of Environmental Quality, Division of Water Quality

Blayde McIntire

has passed the competency examination, and met all further requirements,
to qualify as a

Registered Storm Water Inspector



M. Scott Bird, USWAC Chair

Nov 10, 2022

Expires

Delegation of Authority

I, _____ (name), hereby designate the person or specifically described position below to be a duly authorized representative for the purpose of overseeing compliance with environmental requirements, including the Common Plan Permit, at the _____ construction site. The designee is authorized to sign any reports, stormwater pollution prevention plans and all other documents required by the permit.

_____ (name of person or position)

_____ (company)

_____ (address)

_____ (city, state, zip)

_____ (phone)

By signing this authorization, I confirm that I meet the requirements to make such a designation as set forth in _____ (Reference State Permit), and that the designee above meets the definition of a “duly authorized representative” as set forth in _____ (Reference State Permit).

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

Name:

Company:

Title:

Signature:

Date:

APPENDIX G: BMP Specifications and Details




Label BMPs to match the sections identified in this document.

THESE DRAWINGS AND SPECIFICATIONS ARE THE PROPERTY OF UTAH PROJECTS LOGGERS & ENGINEERS, INC. (UPE) AND ARE NOT TO BE REPRODUCED, COPIED, OR TRANSMITTED IN ANY FORM OR BY ANY MEANS, ELECTRONIC OR MECHANICAL, INCLUDING PHOTOCOPYING, RECORDING, OR BY ANY INFORMATION STORAGE AND RETRIEVAL SYSTEM, WITHOUT THE WRITTEN PERMISSION OF UPE. UPE ASSUMES NO LIABILITY FOR ANY DAMAGE OR LOSS OF PROFITS, BUSINESS, OR REVENUE, OR FOR ANY SPECIAL, INCIDENTAL, OR CONSEQUENTIAL DAMAGES, INCLUDING ATTORNEY'S FEES, ARISING FROM THE USE OF THESE DRAWINGS AND SPECIFICATIONS. UPE'S LIABILITY IS LIMITED TO THE DESIGN AND CONSTRUCTION OF THE PROJECTS DESCRIBED IN THESE DRAWINGS AND SPECIFICATIONS. UPE'S LIABILITY DOES NOT EXTEND TO ANY OTHER PROJECTS OR TO ANY OTHER PARTIES. UPE'S LIABILITY IS LIMITED TO THE DESIGN AND CONSTRUCTION OF THE PROJECTS DESCRIBED IN THESE DRAWINGS AND SPECIFICATIONS. UPE'S LIABILITY DOES NOT EXTEND TO ANY OTHER PROJECTS OR TO ANY OTHER PARTIES.

A NEW DESIGN FOR THE :
SOBEY RESIDENCE
3457 E WESTVIEW TRL.
PARK CITY, UTAH 84098

LOT 20
SIGNAL HILL

UP WALL
DESIGN
1930 S. 1100 E. S.L.C. UT 84106
(801) 485-0708

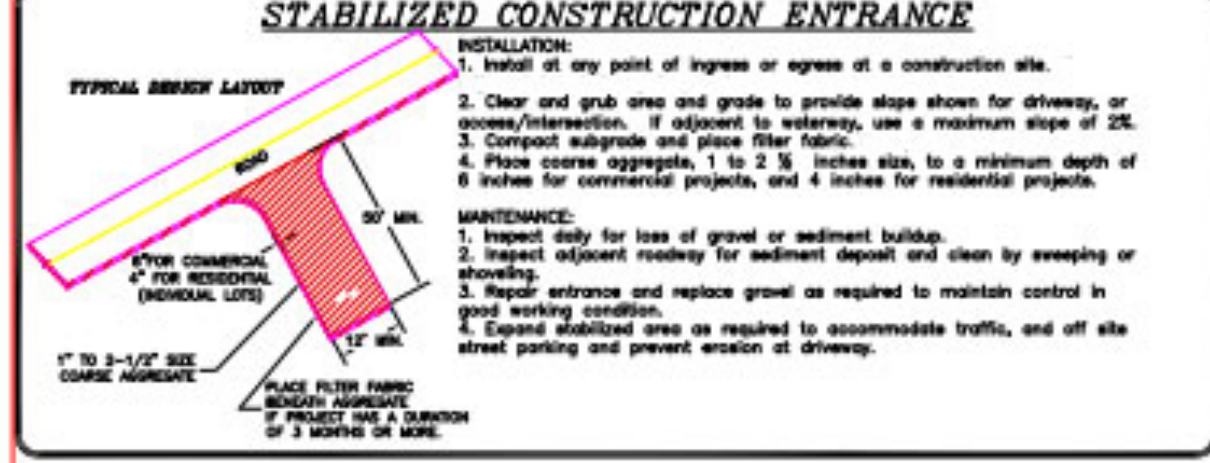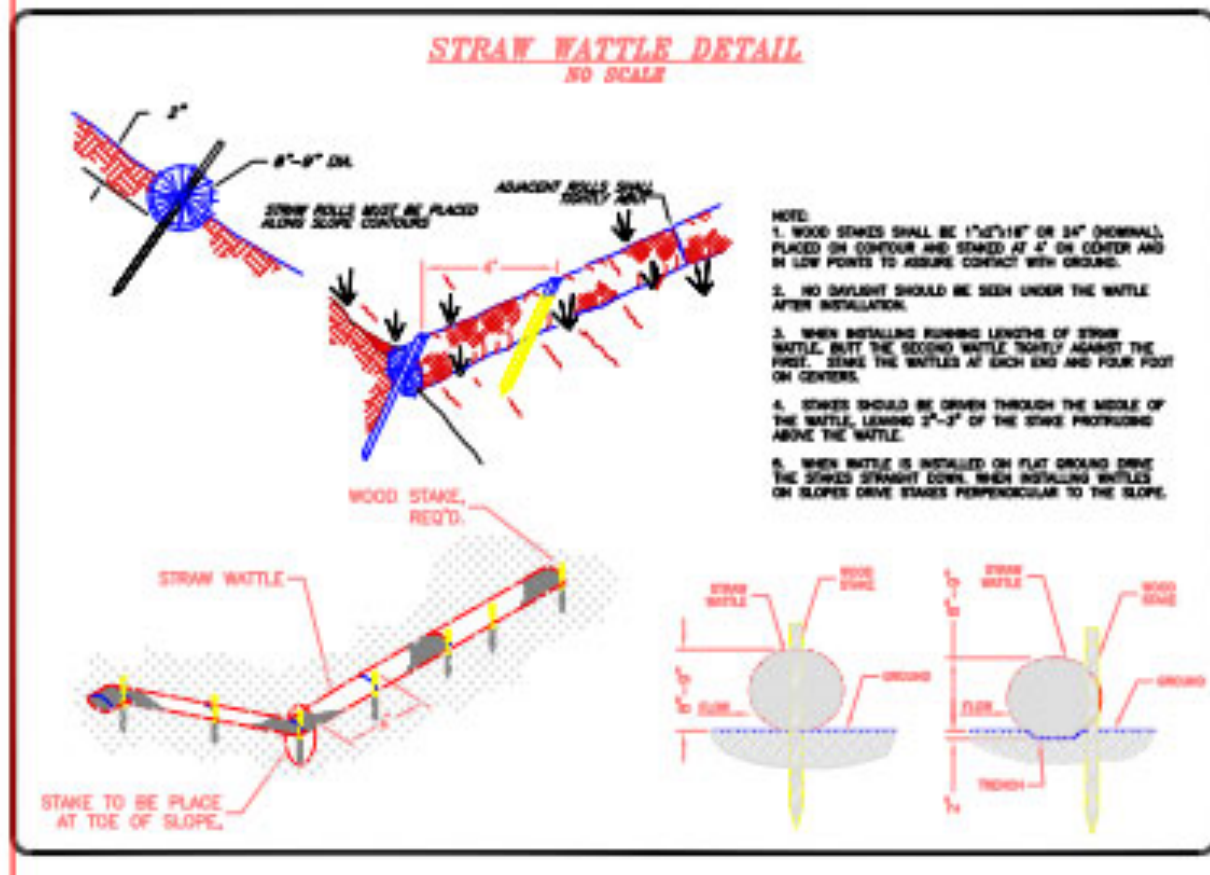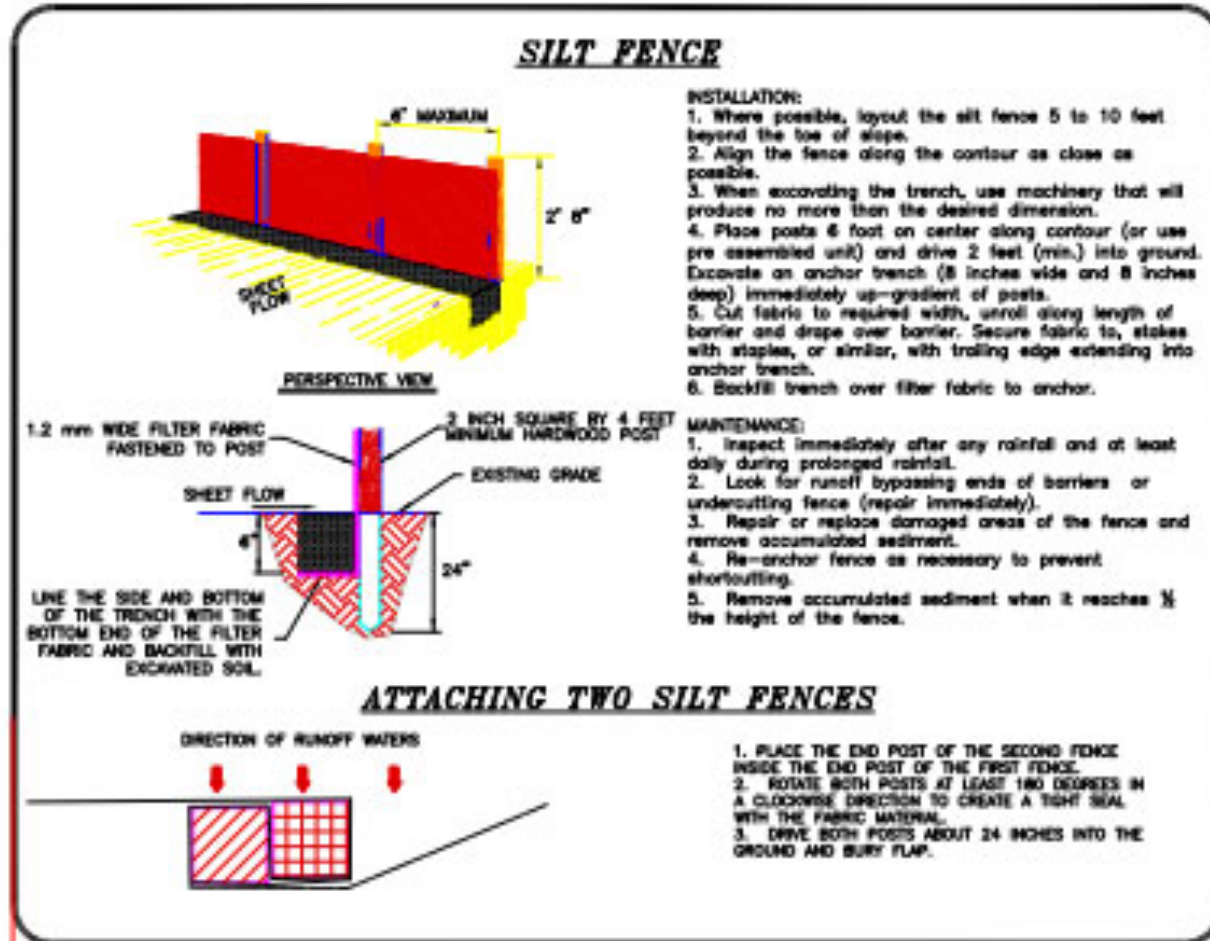

Required Inspections Table




Inspection	Description/Requirements	Contact
Driveway/ Site Staking	Required prior to issuance of a Building Permit. Locate stake the driveway at the street and at the road right of way/property line and locate/stake all property corners.	Engineering
Rough Grading	Required prior to scheduling a Final Inspection. Site Erosion Control measures must be installed and driveway must be roughly graded according to Plan.	Engineering
Footings	Schedule after steel is in place and before the concrete is poured.	Building
Foundations	Schedule after steel is in place in the forms and before concrete is placed.	Building
Under Slab Plumbing & Heating	Before concrete is poured or plumbing has been backfilled.	Building
Certificate of Occupancy and/or Fire	Performed by a licensed surveyor. Request prior to scheduling a Final Inspection. See my comments below.	Building
Floor Framing Inspection	Required prior to placing floor sheathing and includes footing. Draw inspection.	Building
Shear Wall	After the building is up to "the square" and all shear walls have been sited and all tie downs and shear wall connections have been installed.	Building
Fire Sprinklers	Required prior to leak water inspection, when required by the local Fire District.	Building
Four Way	This inspection is performed after all rough electrical, plumbing, and mechanical has been installed. All framing is complete, shear walls previously inspected, and most specifications are on the job for the inspector to read. Flashing shall have either air or water pressure test or then when the inspector arrives.	Building
Weather Barrier/Window Lath	Weather barrier shall be inspected prior to applying window. Appointed check I.C.C. inspector reports on site.	Building
Gas Meter Set	Required before gas meter clearance is given to Gasmaster.	Building
Masonry and/wood beam	Steel in masonry and before concrete/pour is placed.	Building
Insulation	Pro-Shotrock, insulation certificate required.	Building
Driveway Nailing	This is done before gravel is laid.	Building
Proven to Pass	Building must be up with permanent roof installed.	Building
Driveway pre-surfacing	Site Erosion Control measures must be installed and driveway graded to it's final configuration.	Engineering
Final Driveway and Site Inspection	Required prior to Certificate of Occupancy and/or Final Release. Driveway must be surfaced and site must be re-vegetated (inspections may be scheduled separately). If the site is not re-vegetated, the erosion control measures must be in place and installed correctly.	Engineering
Flood Plain Elevation Certificate	FEMA Elevation Certificate (if applicable) required prior to Certificate of Occupancy. Forms must be filed with FEMA and a copy provided to the Engineering Department.	Engineering
Final	All work is DONE and building complete. Final clearances from the waste water district for sewer, County Health Department for septic, and fire district for sprinkler systems must be on the project for this inspection. Required for Certificate of Occupancy.	Building
Certificate of Occupancy	Required prior to anyone occupying the structure. A Certificate of Occupancy will be issued once the final clearances have been obtained by the holder and brought to the Building Department's office in Cash-ite. 1) Snowville Basin Residential: Final from Building Department, Final from Engineering Department, Final from Basin Water Reclamation District, Final from Basin Water Reclamation District, Final from Basin Water Reclamation District, Final from Basin Water Reclamation District. 2) Eastern Summit County: Final from Building Department, Final from Engineering Department, Final from Fire District and Final from Health Department.	Building
ECP Final Release Inspection	Required to verify that the site has been fully stabilized (re-vegetated). Inspection is required prior to applicant receiving a release of their Erosion Control Bond. Applicant must provide a written record for the release of the bond.	Engineering

Construction Mitigation Plan Notes

- Show location for dumpster, portable toilets, materials storage, parking.
- Construction parking traffic may not block the street without a permit (available from the Engineering Division).
- Mud trucked out onto the street must be cleaned prior to the end of the work day.
- The construction site must be maintained in a neat manner. Trash and other debris may not accumulate outside the dumpster.
- Roadside parking is not allowed from November 1st to April 1st.

Concrete washout areas may be prefabricated concrete washout containers, or self-installed structures (above-grade or below-grade).


- Prefabricated containers are most resistant to damage and protect against spills and leaks. Companies may offer delivery service and provide regular maintenance and disposal of solid and liquid waste.
- If self-installed concrete washout areas are used, below-grade structures are preferred over above-grade structures because they are less prone to spills and leaks.
- Self-installed above-grade structures should only be used if excavation is not practical.

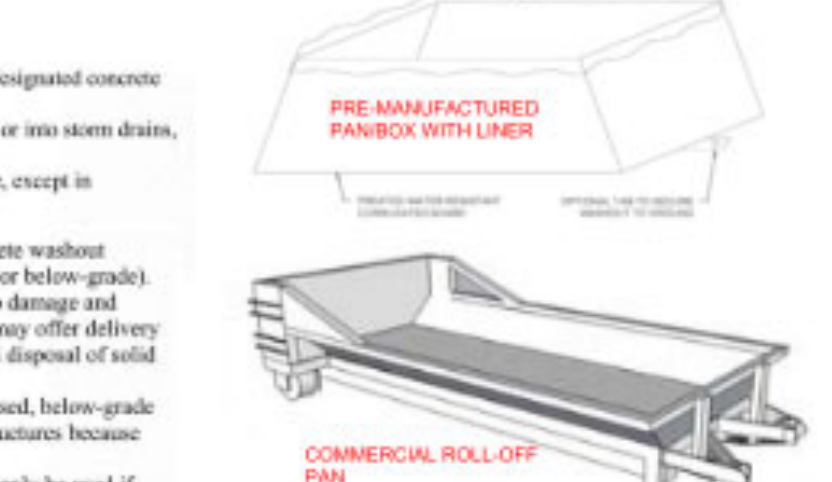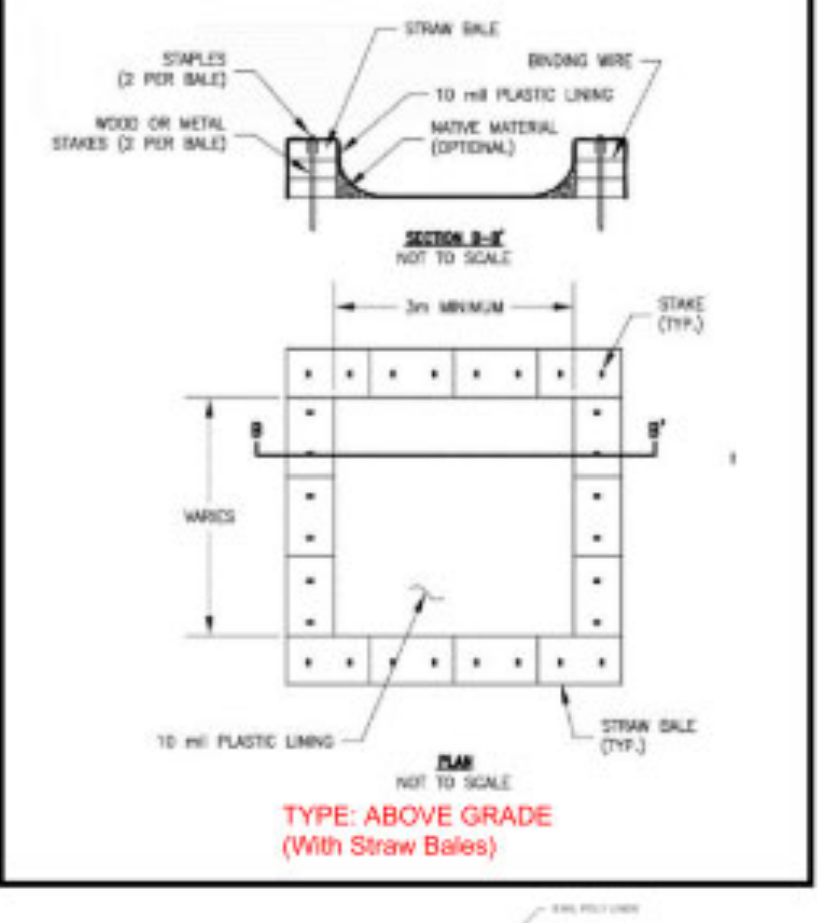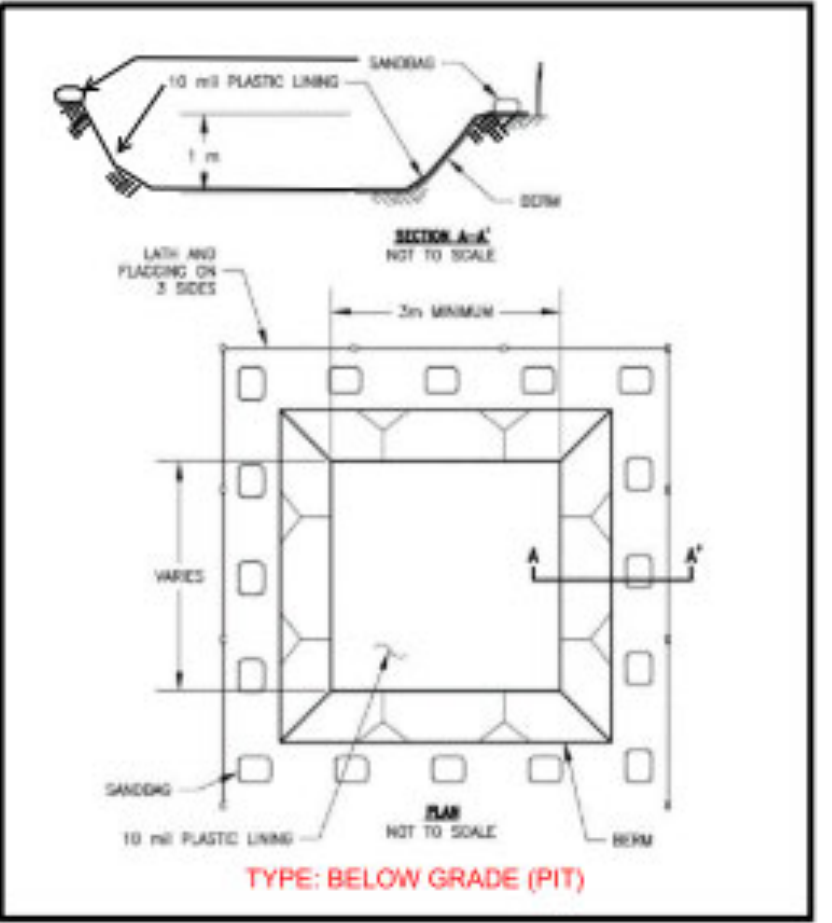

Summit County, Utah
Department of Public Works
Division of Engineering

Summit County
Standard Drawing
Residential Erosion Control Plan

SHEET NO:
SC-1

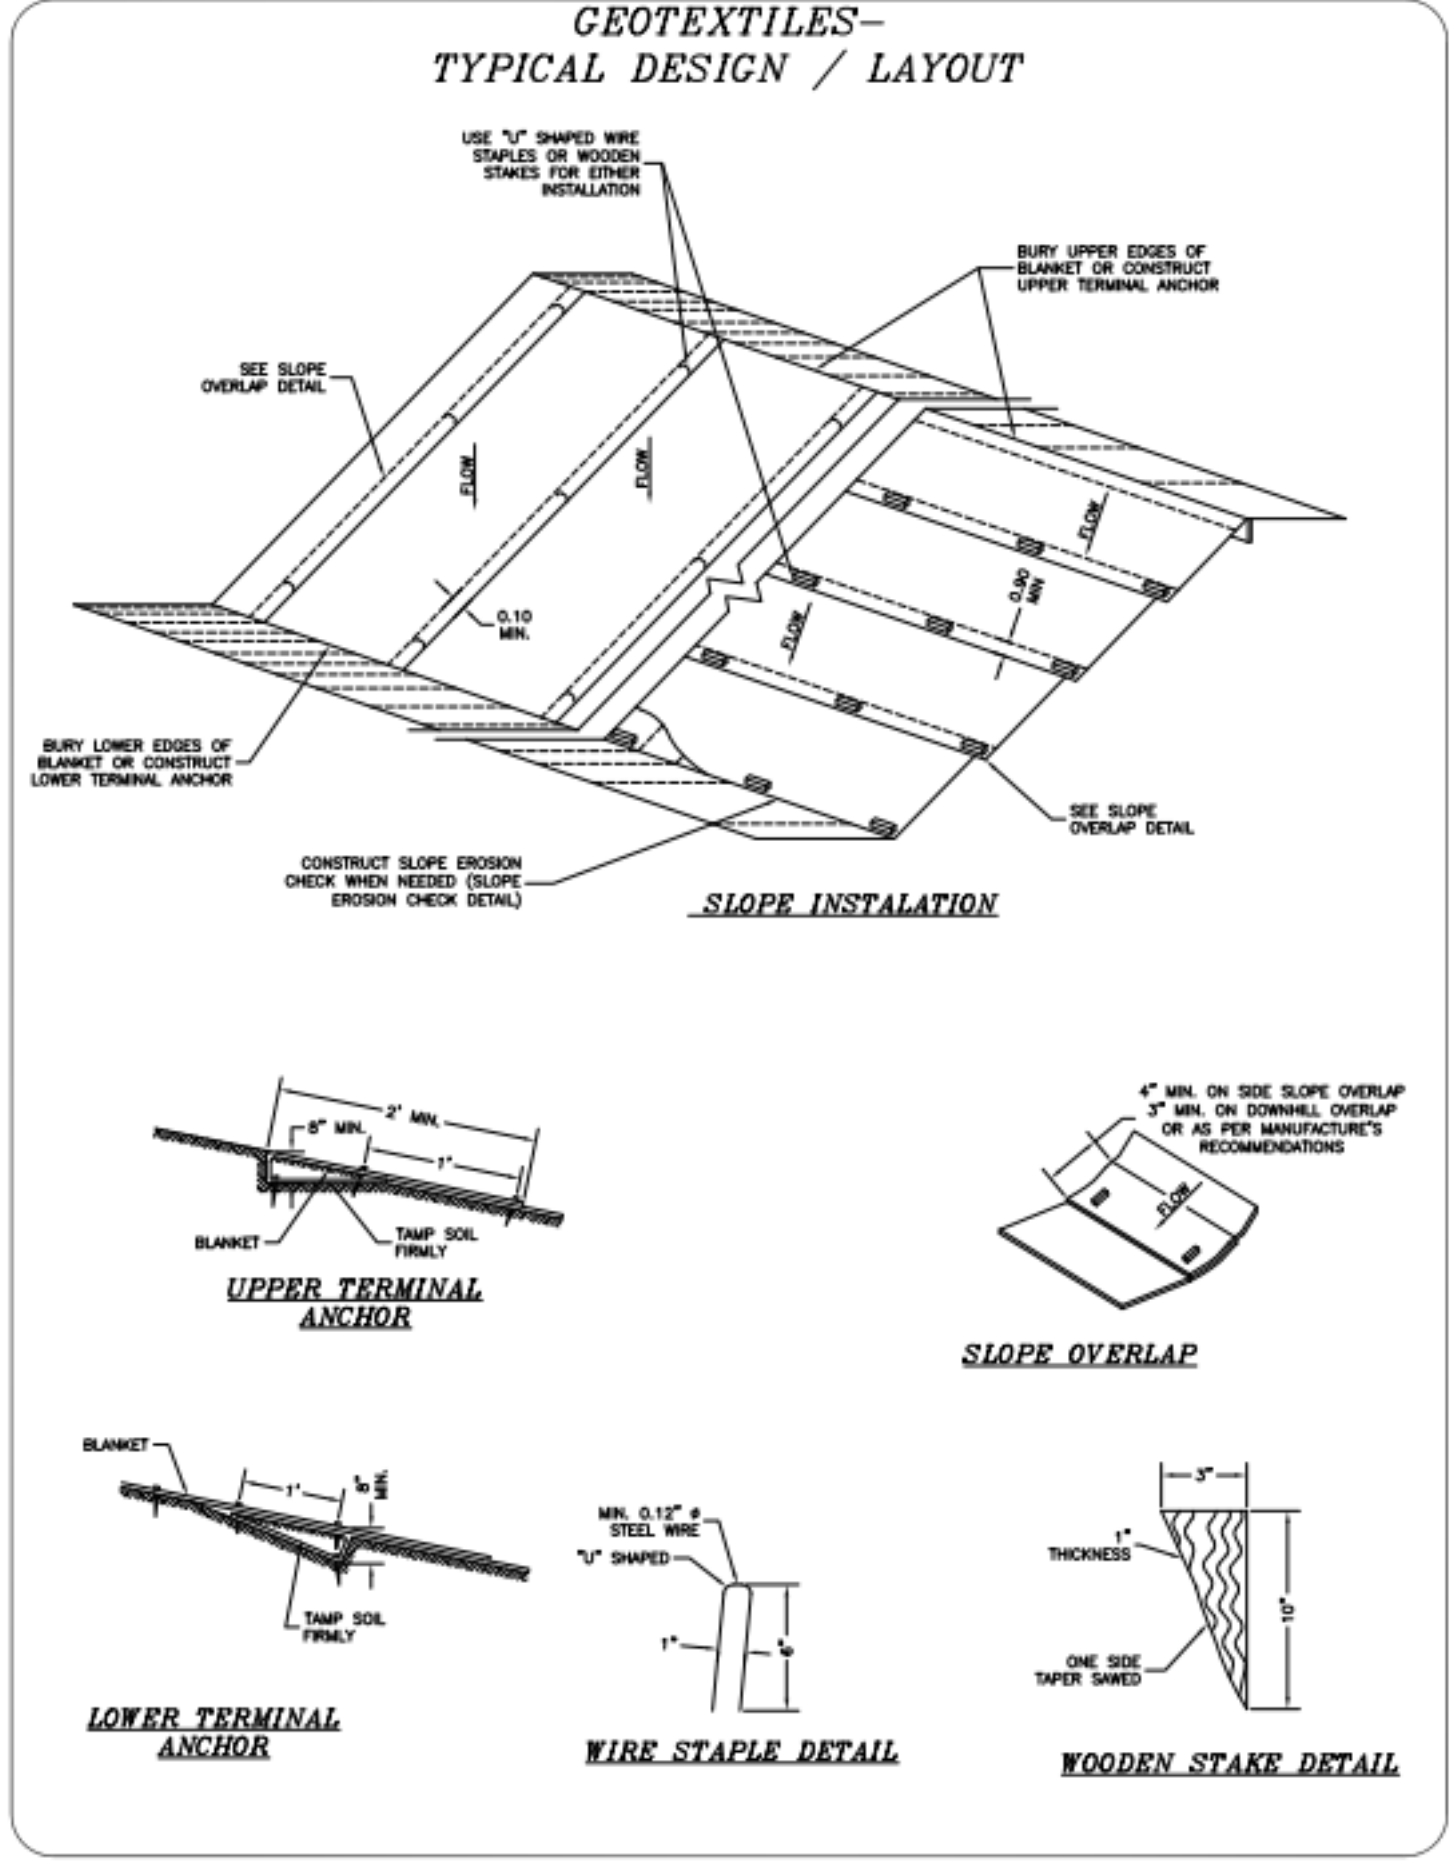

Below are links to various Construction Storm Water BMP Manuals for reference.

Salt Lake County

http://slco.org/uploadedFiles/depot/publicWorks/engineering/final_bmp_constructi.pdf

BEST MANAGEMENT PRACTICES FOR CONSTRUCTION ACTIVITIES

Davis County

http://www.daviscountyutah.gov/docs/librariesprovider20/default-document-library/stormwater-best-management-practices.pdf?sfvrsn=c9cd4053_2

A Guide to Stormwater Best Management Practices

Nevada DOT

<https://www.nevadadot.com/home/showdocument?id=9417>

Stormwater Quality Manuals: Construction Site Best Management Practices (BMPs) Manual

Caltrans

<http://www.dot.ca.gov/hq/construc/stormwater/CSBMP-May-2017-Final.pdf>

Construction Site Best Management Practices (BMP) Manual

Oregon

<http://www.oregon.gov/deq/FilterPermitsDocs/BMPManual.pdf>

Construction Stormwater Best Management Practices Manual

Los Angeles

<http://dpw.lacounty.gov/cons/specs/BMPManual.pdf>

Construction Site Best Management Practices (BMPs) Manual

Maricopa County (Arizona)

<https://www.maricopa.gov/DocumentCenter/View/2368/2015-03-Drainage-Design-Manual-for-Maricopa-County-Volume-III-Erosion-pdf>

Drainage Design Manual for Maricopa County (Erosion Control)

Minnesota

<https://www.pca.state.mn.us/sites/default/files/wq-strm2-09.pdf>

Stormwater Compliance Assistance Toolkit for Small Construction Operators
