

(This SWPPP Template is for the **Common Plan** Permit Only, and
does **NOT** address SWPPP requirements found in the CGP.)

Common Plan SWPPP for Marcella Lot 7

Project Address: 8669 N Ski Beach Way
Heber City, UT 84032

McNulty Construction Company

1526 W. Ute Blvd. Ste. 206
Park City, UT 84098

NOI Permit Number UTRH08269

July 3, 2024



1. Project Information

Project Name: [Marcella Lot 7](#)

Project Address: [8669 N Ski Beach Way](#) [Heber City, UT 84032](#)

General Contractor: [McNulty Construction Company](#)

Contact Person: [Mike McNulty](#)

Address: [1526 W. Ute Blvd. Ste. 206](#) [Park City, UT 84098](#)

Telephone Number: [435-659-9765](#)

Email Address: mike@mmconst.com

Answering “yes” to the question below means the project is not eligible for this permit.

Is the project in Indian Country? Yes No

Answering “no” to the question below means the project is not eligible for this permit.

Is the project a residential building on a single lot and disturbing one acre or less? Yes No

2. Pollution Sources/Best Management Practices

Answer yes or no whether the following features are located at your site. If yes, select the BMP(s) that will be used to protect each feature. If no, continue to the next question. Attach necessary illustrated details for proper installation in Appendix G, and show locations of all controls on Site Map in Appendix A.

2.1 Is there a SWPPP sign on site? (see permit part 1.10) Yes Required

The sign must include the UPDES tracking number, the owner or general contractor name, phone number and email, and if the SWPPP is on-line, instructions on how to view it. The size requirement is to be readable from a publicly accessible point.

2.2 Will there be construction dewatering on the site? (see permit part 2.7) Yes No

BMP(s): Dewatering of the construction area is needed and a separate dewatering permit has been obtained to treat and discharge water. *Construction Dewatering (if discharged offsite) must be covered by UPDES Permit UTG070000.*
 Water from the dewatering of the construction area will be infiltrated on site.

2.3 Will there be non-storm water discharges on the site? (see permit part 1.3) Yes No

Allowable discharges include: Flushing of drinking water or irrigation water (not including wash or cleaning waters), water used for dust control, spring water or groundwater not exposed to construction activities, water from emergency fire-fighting activities, and water from foot drains not exposed to construction activities. (see permit part 2.4.5 & 2.9).

Please list all anticipated non-storm water discharges: [Click here to enter text.](#)

What will you do to manage the non-storm water discharges? *Please list direct discharges, contained non-storm water discharges, and discharges that are treated separately.*

BMP(s): All non-storm water discharges are listed as allowable per permit part 1.3 and discharged

Storm Water Pollution Prevention Plan Template (SWPPP)
Common Plan Permit

- All non-storm water discharges that are not allowed are properly contained (see questions 2.12 and 2.16)
- All non-storm water discharges that are contaminated with sediment only (free of chemicals, oils, etc.) will be treated in a sediment basin or equivalent (see permit part 2.8.1).
- Other: [Click here to enter text.](#)

2.4 Is it possible for the total area of disturbance to be phased, minimizing the total exposure of disturbed soil at one time? (see permit part 2.3.1) Yes No
If disturbance can be minimized please show the locations on the site map and summarize (here) where disturbances will be delayed for some of the disturbed area: [Click here to enter text.](#)

2.5 What perimeter controls will be used to prevent sediment from leaving the site? (permit part 2.1.2 & 2.3)

- BMP(s):**
- | | |
|---|---|
| <input checked="" type="checkbox"/> Silt Fence | <input type="checkbox"/> Berms |
| <input checked="" type="checkbox"/> Vegetative Buffer | <input type="checkbox"/> Cut-Back-Curb |
| <input type="checkbox"/> Staked straw Wattles (Fiber Rolls) | <input type="checkbox"/> Weighted Wattles |
| <input type="checkbox"/> Other: Click here to enter text. | |

2.6 Are surface waters located within 30 feet of your project's earth disturbances? Yes No

Note: A 30' natural vegetative buffer MUST be maintained by water bodies. If a buffer less than 30' is used, you must demonstrate that the additional controls offer the same protection as a 30' natural vegetative buffer, and select the reason for exemption below. (see permit part 2.3.5)

- BMP(s):**
- 30' Natural Vegetative Buffer
- If less than 30' Natural Vegetative Buffer select additional Controls:
- | | |
|---|---|
| <input type="checkbox"/> 2 Silt Fence Barrier | <input type="checkbox"/> 2 Straw Wattle Barriers (Fiber Roll) |
| <input type="checkbox"/> Other: Click here to enter text. | |

2.7 Are there critical or sensitive areas (such as preservation of the drip lines around trees, wetlands, buffer zones by water bodies, etc.) located on or adjacent to the site? (see permit part 2.2) Yes No

- BMP(s):**
- Separate and isolate with environmental fencing
 - Other: [Click here to enter text.](#)

2.8 What track out control will be used to prevent dirt from being tracked on streets as vehicles leave the site? (see permit part 2.4.1)

- BMP(s):**
- | | | |
|---|---|--|
| <input type="checkbox"/> Track Out Pad | <input checked="" type="checkbox"/> Cobble | <input checked="" type="checkbox"/> Gravel |
| <input type="checkbox"/> Rumble Strips | <input type="checkbox"/> Wash Down Pad | <input type="checkbox"/> Delivery Pad |
| <input type="checkbox"/> Restricted Site Access | <input type="checkbox"/> Selective Access During Dry Weather (Dry soil) | |
| <input type="checkbox"/> Other: Click here to enter text. | | |

2.9 Do you have storm drain inlets on or down gradient of this site? (see permit part 2.1.3) Yes No

Protection must address the curb inlet opening (throat) as well as the grate.

Where is/are the nearest downstream inlet(s) and how will you protect them: There are 2 inlets approximately 200 feet downhill from the property

- BMP(s):**
- | | |
|--|---|
| <input type="checkbox"/> Rock/Sand-filled Bags | <input type="checkbox"/> Drop Inlet Bags |
| <input type="checkbox"/> Filter Fabric | <input checked="" type="checkbox"/> Gravel or Sand filled Wattles |

Storm Water Pollution Prevention Plan Template (SWPPP)
Common Plan Permit

- Proprietary inlet devices
- Other: [Click here to enter text.](#)

2.10 Will curb ramps be used at the site? (see permit part 2.4.2) Yes No
If curb ramps are used it must be done with material [not dirt] that will not wash away in storm water.
BMP(s): Crushed Rock Wood/Steel Ramps
 Other: [Click here to enter text.](#)

2.11 Will there be stockpiles or spoil piles on the site? Yes No
Note: Select "Contained by other BMP" if another BMP on your site will contain runoff from the stockpiles. Materials that can be transported with precipitation must not be placed in the street. (see permit part 2.1.1)
BMP(s): Surrounded by Silt Fence Surrounded by Staked Straw
 Covered with Tarp Wattles
 Temporary – Removed same day
 Contained by other BMP. Explain: Silt fence is already planned downgradient of all construction activity, and will therefore also contain runoff from stockpiles
 Other: [Click here to enter text.](#)

2.12 Does the project include installation of concrete, masonry, stucco, and paint (water based)work in this project? (see permit part 2.4.5 & 2.9.1) Yes No
Wash water must be contained, the solids dried, and disposed of at a landfill.
BMP(s): Lined Depression Steel Dumpster
 Regional Washout (per development)
 Other: Eco pan is specified, but any equivalent washout is permitted

2.13 How will solid waste be dealt with on the site? (see permit part 2.4.3)
Light trash in uncovered dumpsters can blow out and scatter with wind and rain may fall on uncovered leachable material in the dumpster and leak out the bottom causing pollutants to escape.
BMP(s): Bag Lightweight Trash Leak Proof Dumpsters
 Receptacles with Lids Other: [Click here to enter text.](#)

2.14 Will there be a need to dispose of solvents, oil, fuel, etc. liquid waste? (see permit part 2.9) Yes No
BMP(s): Contained and Removed from the site Collected for Reuse
 Other: [Click here to enter text.](#)

2.15 How will sanitary waste be handled on the site? (see permit part 2.4.4)
BMP(s): Portable Toilet(s) (*must be staked down on dirt surface & 10' from curb*)
 Onsite or Adjacent Indoor Bathrooms
 Portable Toilet Secondary Containment (secured down with straps to heavy weights)
 Other: [Click here to enter text.](#)

2.16 How will you minimize the discharge of pollutants from spills and leaks? (see permit part 2.8.3)
BMP(s): Use of drip pans Offsite fueling, and maintenance
 Spill kit Spill response plan.
 Other: [Click here to enter text.](#)

2.17 Will there be a need to store construction materials on site? (see permit 2.8.2) Yes No

Storm Water Pollution Prevention Plan Template (SWPPP)
Common Plan Permit

Minimize the exposure of materials with a pollution risk (certain building and landscaping materials, fertilizers, pesticides, herbicides, detergents).

- BMP(s):** Covering Erodible or Liquid Materials Secondary Containment
 Strategic Storage and Staging Stored off-site
 Enclose them in a weather proof shed.
 Other: [Click here to enter text.](#)

2.18 Does your site have steep slopes (greater than 70%)? (see permit part 2.3.2) **Yes** **No**

- BMP(s):** Erosion Control Blanket Avoid Disturbance on slope
 Seeding Hydroseed
 Mulch Takifiers
 Other: [Click here to enter text.](#)

2.19 Are there site conditions that cause storm water flows with highly erosive velocities? (see permit parts 2.3.3 and 2.3.4) **Yes** **No**

Flows must be controlled to minimize sediment transport.

- BMP(s):** Gravel Check Dam Straw Wattles (Fiber Rolls) Check Dam
 Divert Flows around the Site Armored channel (riprap, geotextile, other)
 Other: [Click here to enter text.](#)

2.20 How will you reduce storm water volume to minimize sediment transport, channel and stream bank erosion? (see permit parts 2.3.4 and 2.3.3)

- BMP(s):** Utilize basin, depression storage of storm water, cut back curb, or other to hold and infiltrate.
 Prevent heavy equipment (as much as possible) from compacting soil so storm water will infiltrate easier.
 Rip soil after heavy equipment has caused compaction.
 Other: [Click here to enter text.](#)

2.21 Is there a need for dust control on the site (regulatory or for practical reasons)? **Yes** **No**

- BMP(s):** Wetting with Water Cover dirt piles with a tarp
 Use Magchloride, Calcium Chloride or Lignan Sulfonate
 Stabilize surface with mulch, gravel or other surface cover
 Other: [Click here to enter text.](#)

2.22 Will there be disturbed areas on the site that will need to be temporarily stabilized before the project is completed? (see permit part 2.6) **Yes** **No**

Places that are disturbed and then left for over 14 days with no activity, must be temporarily or permanently stabilized.

- BMP(s):** Bark or other mulch Hydro-mulch Seeding
 Tackifier Staked netting with straw mulch
 Other: [Click here to enter text.](#)

2.23 Will the house be sold without any landscaping? **Yes** **No**

If so, how will you leave the site for the new home owner so sediment will be contained on site until the home owner completes landscaping? (the permit can be terminated when the owner occupies the house even though the site is not stabilized).

- BMP(s):** Mulching/Hydro-mulching Swales Silt Fence

- Wattles
- Vegetated Buffer
- Other: [Click here to enter text.](#)
- Cut-Back-Curb
- Grade Front-Yard Lower than Sidewalk
- Seeding

3. Sequence of Construction Activity

Type of Construction Activity	Approximate Date Range
Start/End of the Project	July 2024
Excavation activities	July 2024-November 2024
Foundation/Footings	October 2024
Backfill	November 2024
Erection of Building	December 2024 – June 2026
Utility Lines installed	November 2024
Landscaping	Spring 2026

4. Site Map

On a blank page (or include a page from the architectural drawings that show site layout and dimensions), please draw a map (and place this map in Appendix A) showing the layout of the site including locations of:

1. boundaries of project/property
2. boundaries of disturbance (including areas outside of property boundaries)
3. show slopes on site (if there are steep areas show steep areas)
4. location of structures/facilities
5. locations of:
 - a. stockpiles for soils and materials
 - b. construction supplies
 - c. portable toilets
 - d. garbage/trash containers
 - e. egress points/track out pads
 - f. concrete washout pits or containers
6. water bodies, wetlands, natural vegetative buffers
7. placement of all BMPs, perimeter, erosion control, sediment control, inlet protection, etc.
8. storm water inlets and storm water discharge points (where storm water drains off the site)
9. areas that will be temporarily or permanently stabilized on the site

10. areas where disturbances will be delayed to minimize total exposed surface at one time.

5. Potential Sources of Pollutants

Fill out the table below with a pollution prevention method. **Examples include:** Strategic Storage, designated washout area, use only as needed (for fertilizers, etc), or Not Applicable.

Material/Chemical	Storm Water Pollutants	Common Location*	Pollution Prevention Methods
Pesticides (insecticides, fungicides, herbicides, rodenticide)	Chlorinated hydrocarbons, organophosphates, carbamates, arsenic	Herbicides used for noxious weed control	NA – if needed will be stored offsite. Spill plans in place when brought to site.
Fertilizer	Nitrogen, phosphorous	Newly seeded areas	Applied when no rain is forecast. Stored offsite. Prevent from leaving site with vegetative buffer.
Plaster	Calcium sulphate, calcium carbonate, sulfuric acid	Building construction	Captured by onsite stormwater retention, prevented from leaving site, spills cleaned immediately
Cleaning solvents	Perchloroethylene, methylene chloride, trichloroethylene, petroleum distillates	No equipment cleaning allowed in project limits	NA – equipment will be cleaned off site
Asphalt	Oil, petroleum distillates	Streets and roofing	Stored offsite, will be immediately paved and compacted
Concrete	Limestone, sand, pH, chromium	Curb and gutter, building construction	Concrete washout
Glue, adhesives	Polymers, epoxies	Building construction	Spill prevention and cleanup plan
Paints	Metal oxides, Stoddard solvent, talc, calcium carbonate, arsenic	Building construction	Spill prevention and cleanup plan
Curing compounds	Naphtha	Curb and gutter	NA
Wood preservatives	Stoddard solvent, petroleum distillates, arsenic, copper, chromium	Timber pads and building construction	Spill prevention and cleanup plan
Hydraulic oil/fluids	Mineral oil	Leaks or broken hoses from equipment	Spill prevention and cleanup plan
Gasoline	Benzene, ethyl benzene, toluene, xylene, MTBE	Secondary containment/staging area	Spill prevention and cleanup plan

Storm Water Pollution Prevention Plan Template (SWPPP)
Common Plan Permit

Material/Chemical	Storm Water Pollutants	Common Location*	Pollution Prevention Methods
Diesel Fuel	Petroleum distillate, oil & grease, naphthalene, xylenes	Secondary containment/staging area	Spill prevention and cleanup plan
Kerosene	Coal oil, petroleum distillates	Secondary containment/staging area	Spill prevention and cleanup plan
Antifreeze/coolant	Ethylene glycol, propylene glycol, heavy metals (copper, lead, zinc)	Leaks or broken hoses from equipment	Spill prevention and cleanup plan
Sanitary toilets	Bacteria, parasites, and viruses	Staging area	On-site portable toilet will be staked to ground, serviced regularly

*(Area where material/chemical is used on-site)

6. Spill Prevention and Response Plan

Describe who is responsible for containing and cleaning up spills. Provide a specific person’s name and phone number. If a spill kit is located on site, add the location, if there is not a spill kit on site, please provide information on what to use (sand, etc) to contain spills.

Spill Plan:

All equipment and materials will be inspected daily by on-site supervisor (Mike McNulty 435-659-9765). Supervisor will be made aware of any leaks or spills immediately. Spills will be isolated and prevented from spreading. Absorbent material will be placed over the spill and allowed to soak in, then the area will be over-excavated, and the material will be transported to the appropriate disposal location.

Any discharges in 24 hours equal to or in excess of the reportable quantities listed in 40 CFR 117, 40 CFR 110, and 40 CFR 302 will be reported to the National Response Center and the Division of Water Quality (DWQ) as soon as practical after knowledge of the spill is known to the permittee. The permittee shall submit within 14 calendar days of knowledge of the release a written description of: the release (including the type and estimate of the amount of material released), the date that such release occurred, the circumstances leading to the release, and measures taken and/or planned to be taken to the Division of Water Quality (DWQ), 288 North 1460 West, P.O. Box 144870, Salt Lake City, Utah 84114-4870. The Storm Water Pollution Prevention Plan must be modified within 14 calendar days of knowledge of the release to provide a description of the release, the circumstances leading to the release, and the date of the release. In addition, the plan must be reviewed to identify measures to prevent the reoccurrence of such releases and to respond to such releases, and the plan must be modified where appropriate.

Agency	Phone Number
National Response Center	(800) 424-8802
Division of Water Quality (DWQ) 24-Hr Reporting	(801) 538-6146; (801) 536-4123
Utah Department of Health Emergency Response	(801) 580-6681

Storm Water Pollution Prevention Plan Template (SWPPP)
Common Plan Permit

Wasatch County Fire Department	435-940-9636
--------------------------------	--------------

Minimum spill quantities requiring reporting:

Material	Media Released To	Reportable Quantity
Engine oil, fuel, hydraulic & brake fluid	Land	25 gallons
Paints, solvents, thinners	Land	100 lbs (13 gallons)
Engine oil, fuel, hydraulic & brake fluid	Water	Visible Sheen
Refrigerant	Air	1 lb
Antifreeze, battery acid, gasoline, engine degreasers	Air, Land, Water	100 lbs (13 gallons)

Emphasis to:

- 1st Priority: Protect all people (including onsite staff)
- 2nd Priority: Protect equipment and property
- 3rd Priority: Protect the environment

1. Make sure the spill area is safe to enter and that it does not pose an immediate threat to health or safety of any person.
2. Check for hazards (flammable material, noxious fumes, cause of spill) – if flammable liquid, turn off engines and nearby electrical equipment. If serious hazards are present leave area and call 911. LARGE SPILLS ARE LIKELY TO PRESENT A HAZARD.
3. Stop the spill source and contain flowing spills immediately with spill kits, dirt or other material that will achieve containment.
4. Call co-workers and supervisor for assistance and to make them aware of the spill and potential dangers
5. If spilled material has entered a storm sewer, regardless of containment; contact the City Storm Water Division.
6. Cleanup all spills (flowing or non-flowing) immediately following containment. Clean up spilled material according to manufacturer specifications, for liquid spills use absorbent materials AND DO NOT FLUSH AREA WITH WATER.
7. Properly dispose of cleaning materials and used absorbent material according to manufacturer specifications.
8. Report the reportable quantity to the [State of Utah](#) Storm Water Division.

Emergency Numbers

Utah Hazmat Response Officer 24 hrs	(801)-538-3745
Wasatch County Fire Department	435-940-9636
State of Utah Stormwater Division	801-536-4300

7. SWPPP, Inspections and Corrective Action Reports

Inspection Schedule and Procedures: The permit requires inspections **once a week** (see permit Part 3). You must list and provide details of your BMPs in Appendix G.

Describe the general procedures for correcting problems when they are identified. Include responsible staff and time frames for making corrections:

Weekly inspections will be completed by Blayde McIntire of Altitude Engineering (307-679-8620). He will notify site supervisor Mike McNulty of any necessary actions. Actions will be completed within 7 days or before any storm event. Inspections will be filled out on paper and stored in a mailbox on-site near the SWPPP sign.

Inspections and Corrective Actions: All inspections and corrective actions will be noted on the inspection sheet. The site superintendent will be notified immediately of corrective actions and followed up with weekly.

8. Training of Sub-Contractors

All sub-contractors, installers of utility connections, and others that perform activities that are affected by permit requirements will be informed about permit requirements that pertain to their scope of work.

Sub-Contractors are the Responsibility of the NOI holder.

9. Changes to the SWPPP

All changes to this SWPPP must be redlined, dated, and initialed in the SWPPP document and on the site map. All modifications will be stored online on Altitude Engineering's website which is available via QR code on the SWPPP sign.

10. Record Keeping

The following items should be kept at the project site available for inspectors to review:

1. A copy of the Common Plan Permit (A Link is provided in Appendix B)
2. The signed and certified NOI form (Appendix C)
3. Inspection reports (physical, on-site)
4. SWPPP and changes (altitude-engineering.com)

11. Delegation of Authority (if any)

Duly Authorized Representatives or Positions:

Company/Organization: Company of Representative.
Name: Authorized Representative Name.
Position: Representative Title.
Address: Click here to enter text.
City: Click here to enter text. State: State Zip: Zip Code
Telephone: (XXX) XXX-XXXX Fax/Email: (XXX) XXX-XXXX

Owner/General Contractor Signature: _____ Date: _____

Additional Duly Authorized Representatives or Positions:

Company/Organization: Company of Representative.
Name: Authorized Representative Name.
Position: Representative Title.
Address: Click here to enter text.
City: Click here to enter text. State: State Zip: Zip Code
Telephone: (XXX) XXX-XXXX Fax/Email: (XXX) XXX-XXXX

Owner/General Contractor Signature: _____ Date: _____

12. Discharge Information

Does your project/site discharge storm water into a Municipal Separate Storm Sewer System (MS4)?
 Yes No

Municipal Storm Drain System receiving the discharge from the construction project: **Park City**

Receiving Waters (look up <http://mapserv.utah.gov/surfacewaterquality/> to identify your receiving water body).

Enter the name(s) of the first surface water(s) that receives storm water directly from your site and/or from the MS4 listed above. **Note:** *multiple rows provided in the case that your site has more than one point of discharge in which each flows to different surface waters.*

- 1. **Jordanelle Reservoir**
- 2. Click here to enter name of receiving waters.

Storm Water Pollution Prevention Plan Template (SWPPP)
Common Plan Permit


Impaired Waters (refer to <http://mapserv.utah.gov/surfacewaterquality/> in the left hand column to determine status of receiving water body).

Select any impaired surface water(s) that your site will discharge to, either directly or through the MS4 selected above.

Impaired Surface Water	Is this surface water impaired?	Pollutant(s) causing the impairment	Has a TMDL been completed?	Pollutant(s) for which there is a TMDL
Jordanelle Reservoir	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	pH	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	pH

13. Certification and Notification

I, Mike McNulty, certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

DocuSigned by:

7/9/2024
4F3BA593F52744D...
Construction Operator:

This SWPPP should be signed and certified by the construction operator(s).

SWPPP Appendices

Ensure the following documentation is attached to the SWPPP:

Appendix A: SWPPP Site Maps


Appendix B: Common Plan Permit

Appendix C: Notice of Intent (NOI), and a copy of the NOT form unless you plan to terminate the permit on-line

Appendix D: Daily Site Check Log


Appendix G: BMP Specifications and Details (label BMPs to match the sections identified in this document.)

APPENDIX A: SWPPP Site Maps





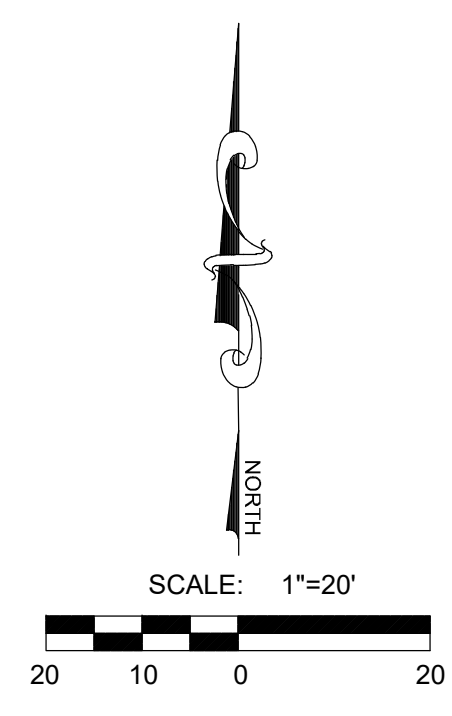


NOTE: DETAILS AND NOTES IN BLUE ON THIS SHEET HAVE BEEN ADDED BY ALTITUDE ENGINEERING FOR THE PURPOSES OF PREPARING A SWPPP DOCUMENT. DATED 07/03/2024.

NOTE: EROSION CONTROL FABRIC IS REQUIRED WHERE SLOPES EXCEED 70%. VERIFY SLOPES ON-SITE.

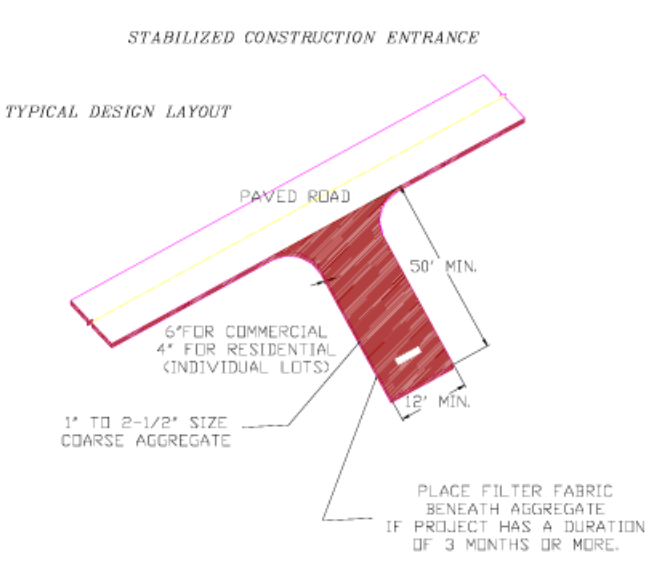

- INSTALLATION:**
1. Install at any point of ingress or egress at a construction site where adjacent traveled way is paved.
 2. Clear and grub area and grade to provide slope shown for driveway, or access/intersection. If adjacent to waterway, use a maximum slope of 2%.
 3. Compact subgrade and place filter fabric if required.
 4. Place coarse aggregate, 1 to 2 1/2 inches size, to a minimum depth of 6 inches for commercial projects, and 4 inches for residential projects.
- MAINTENANCE:**
1. Inspect daily for loss of gravel or sediment buildup.
 2. Inspect adjacent roadway for sediment deposit and clean by sweeping or shoveling.
 3. Repair entrance and replace gravel as required to maintain control in good working condition.
 4. Expand stabilized area as required to accommodate traffic, and off site street parking and prevent erosion at driveway.

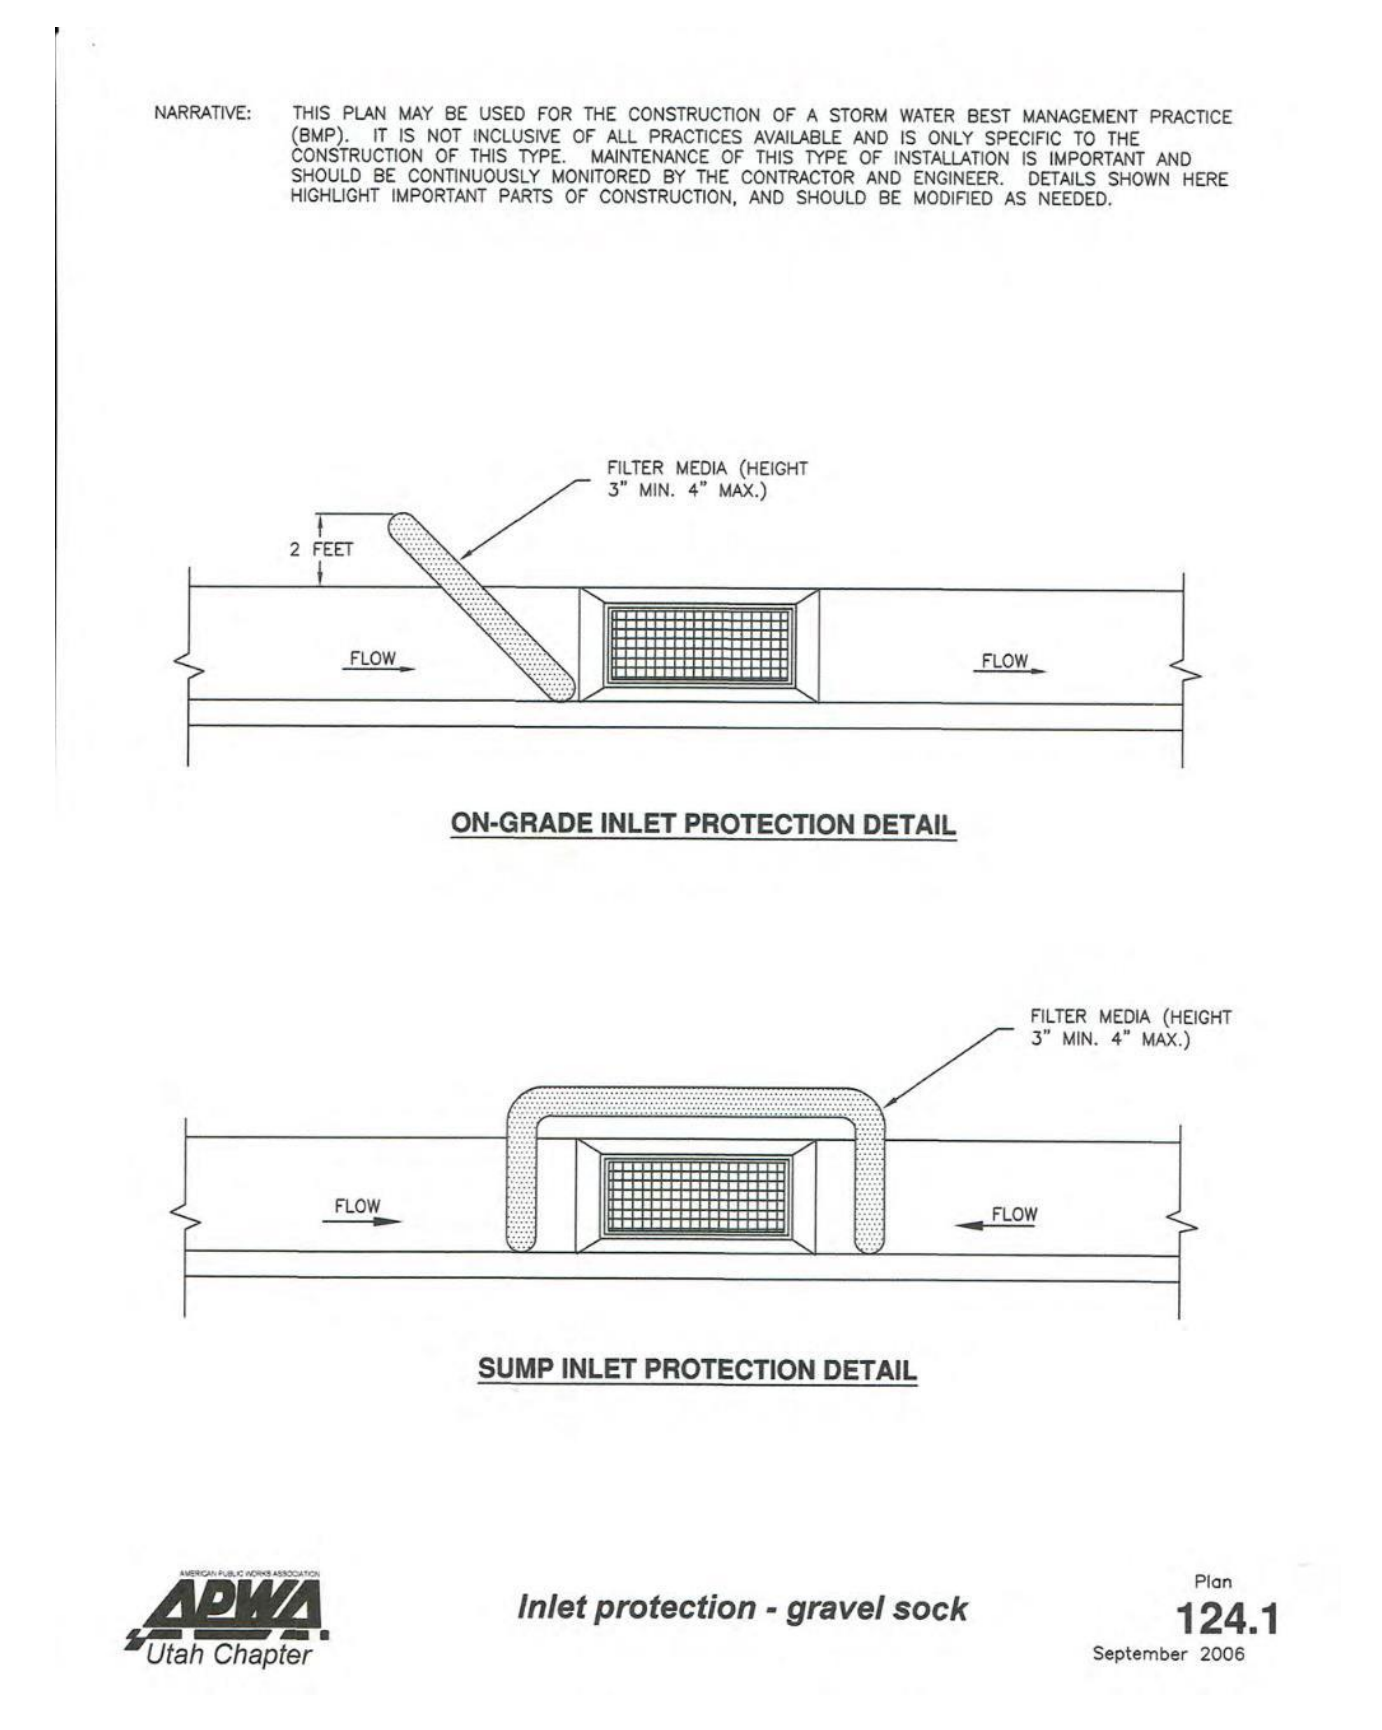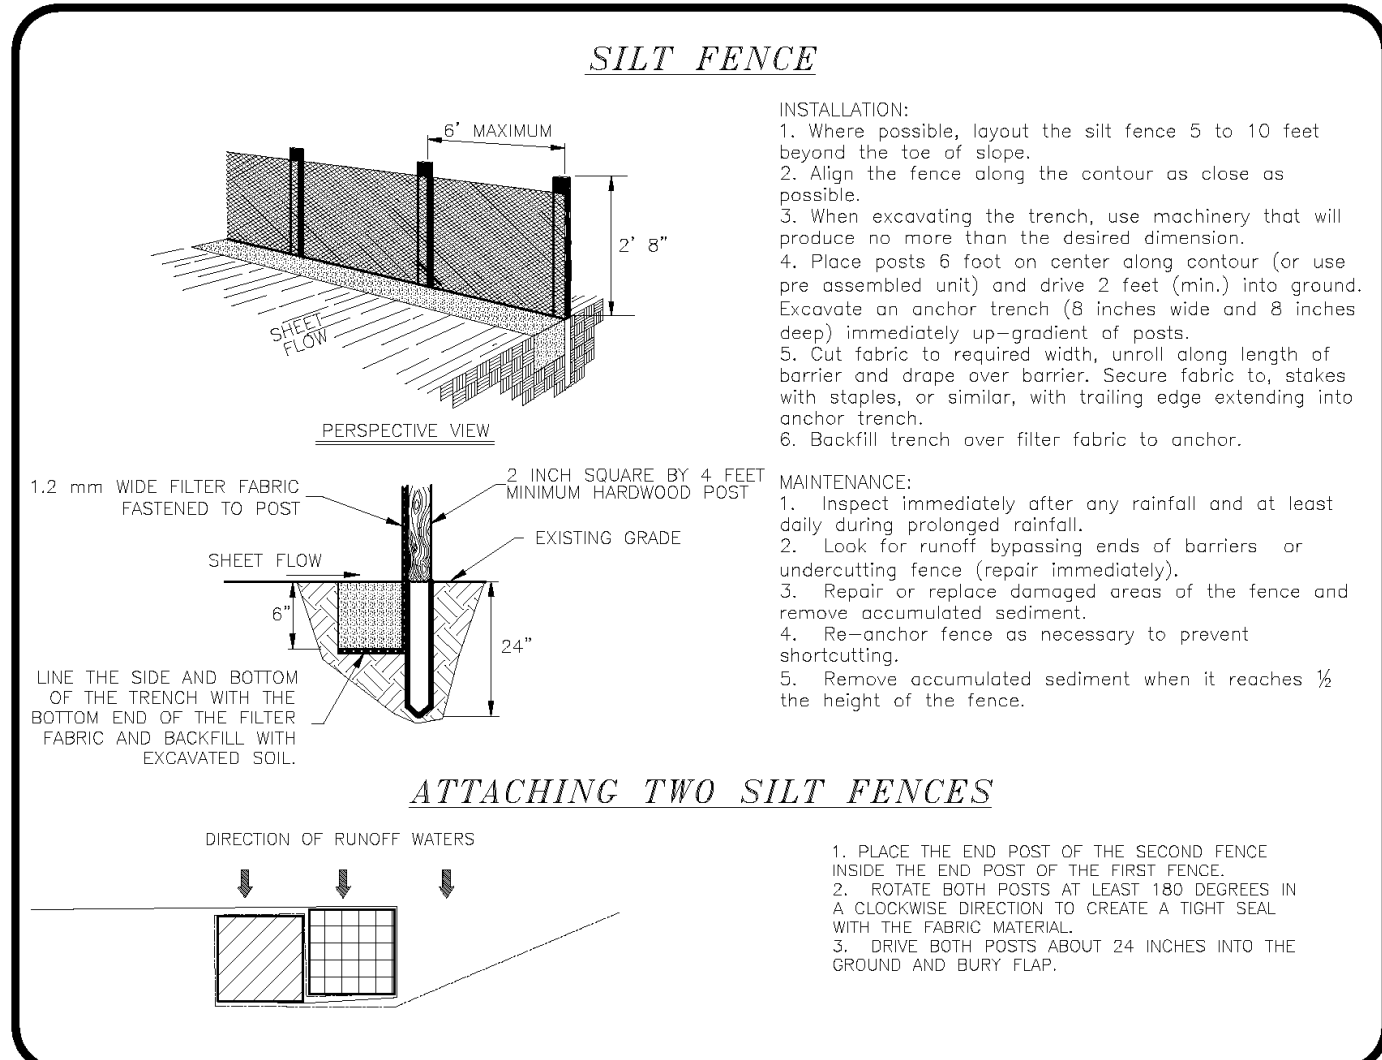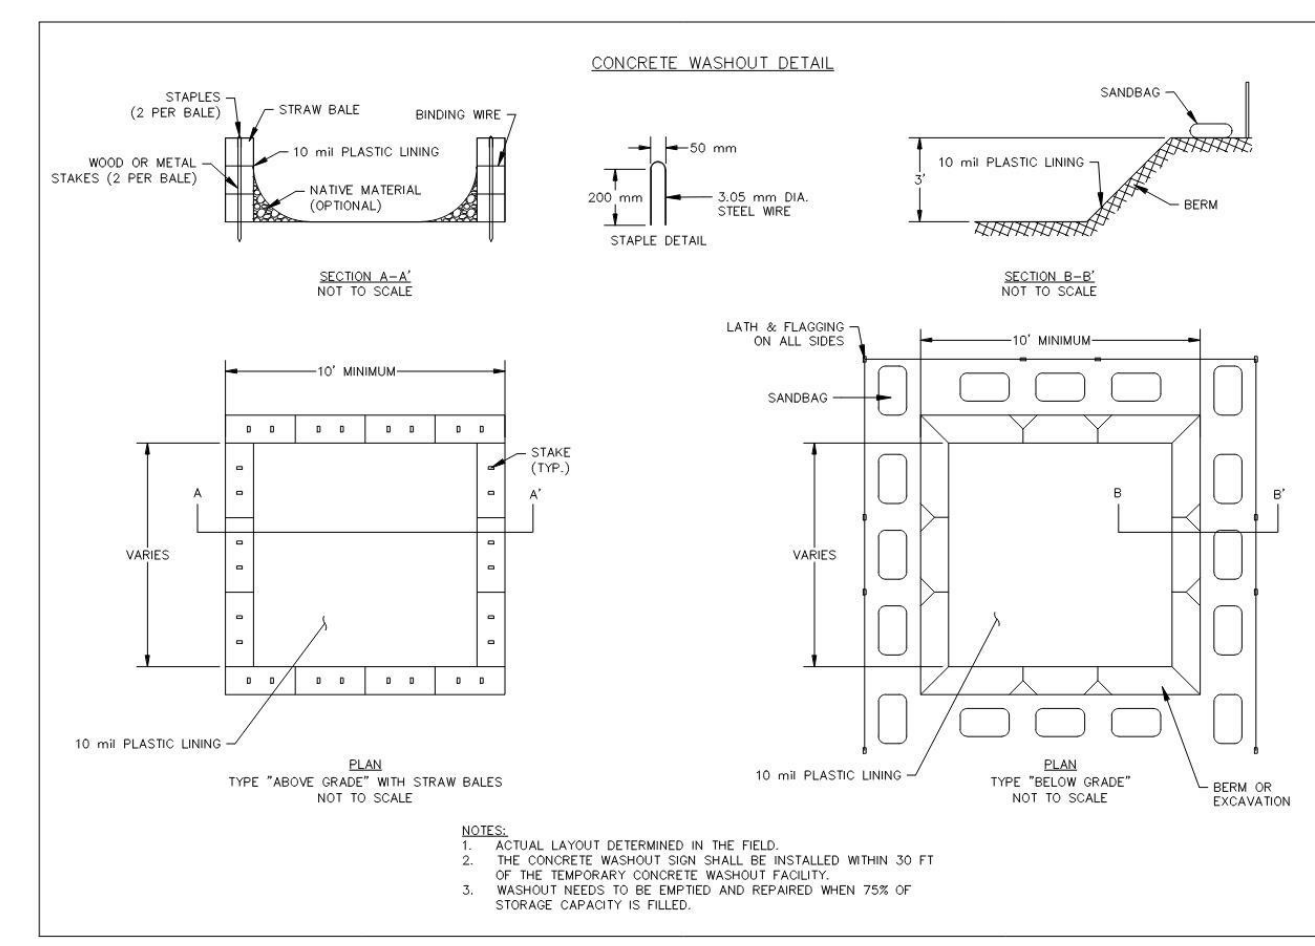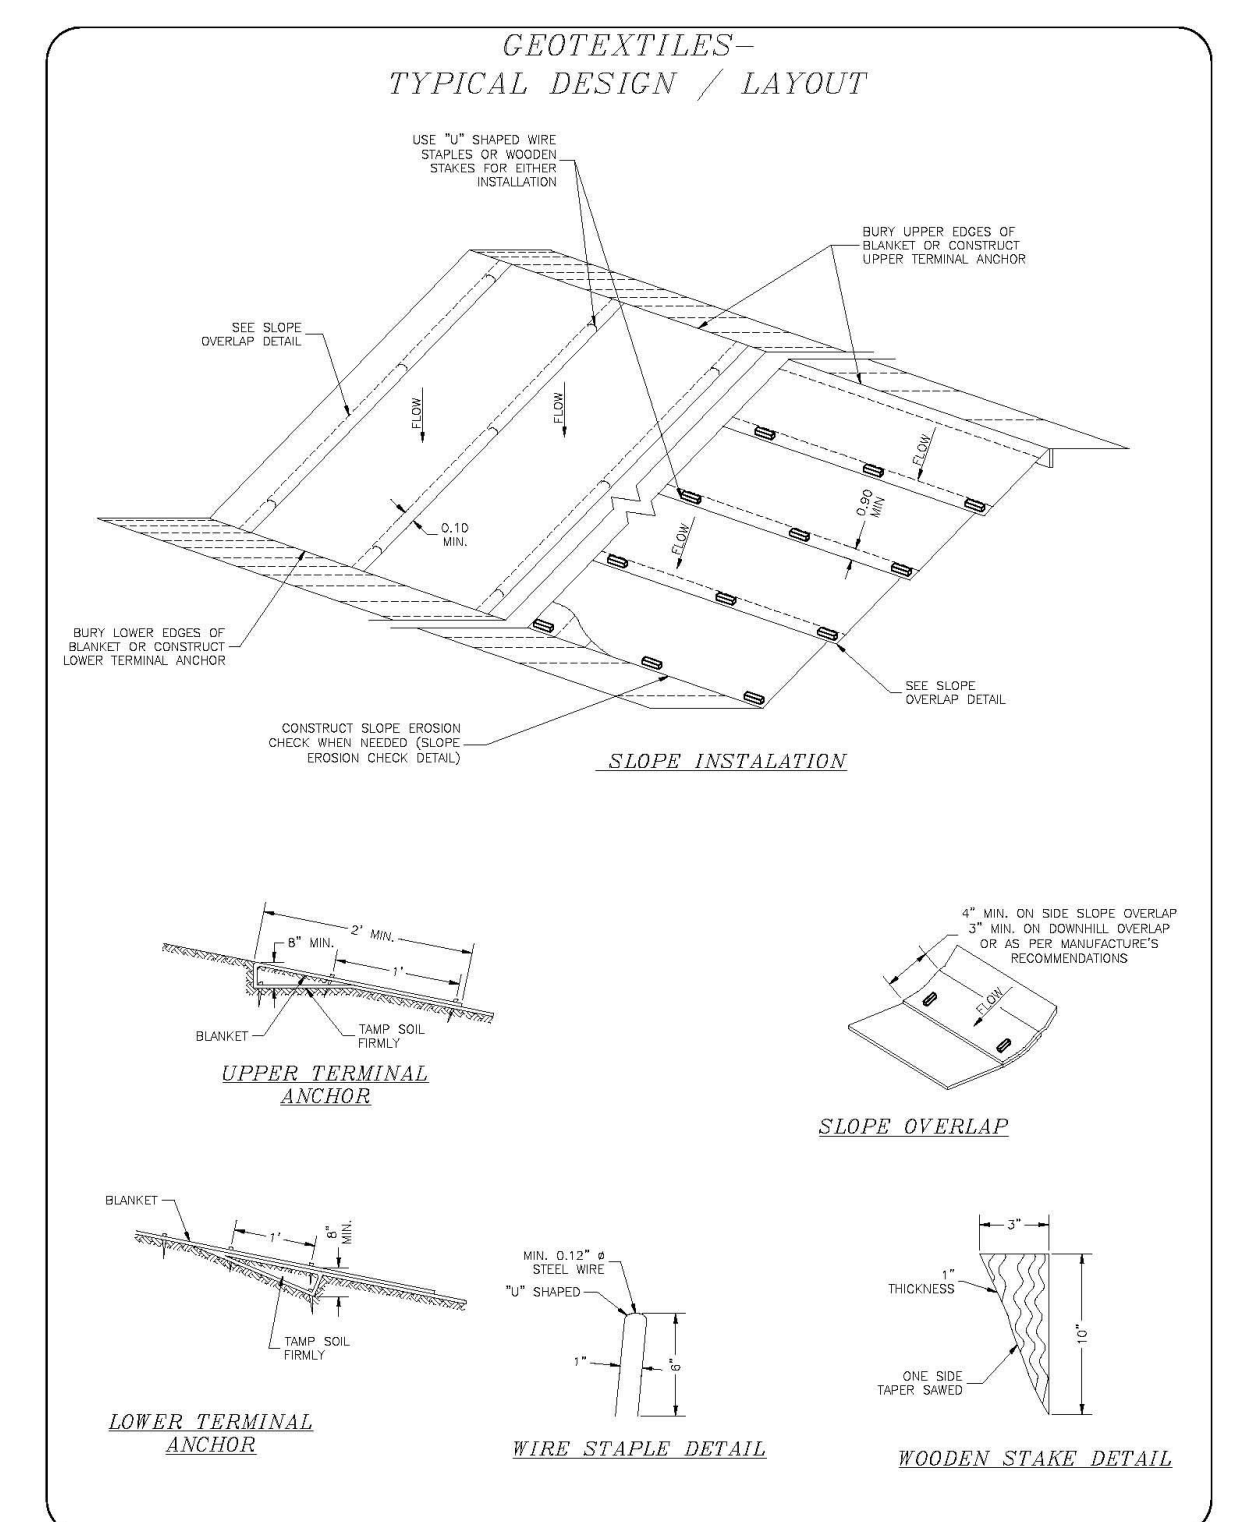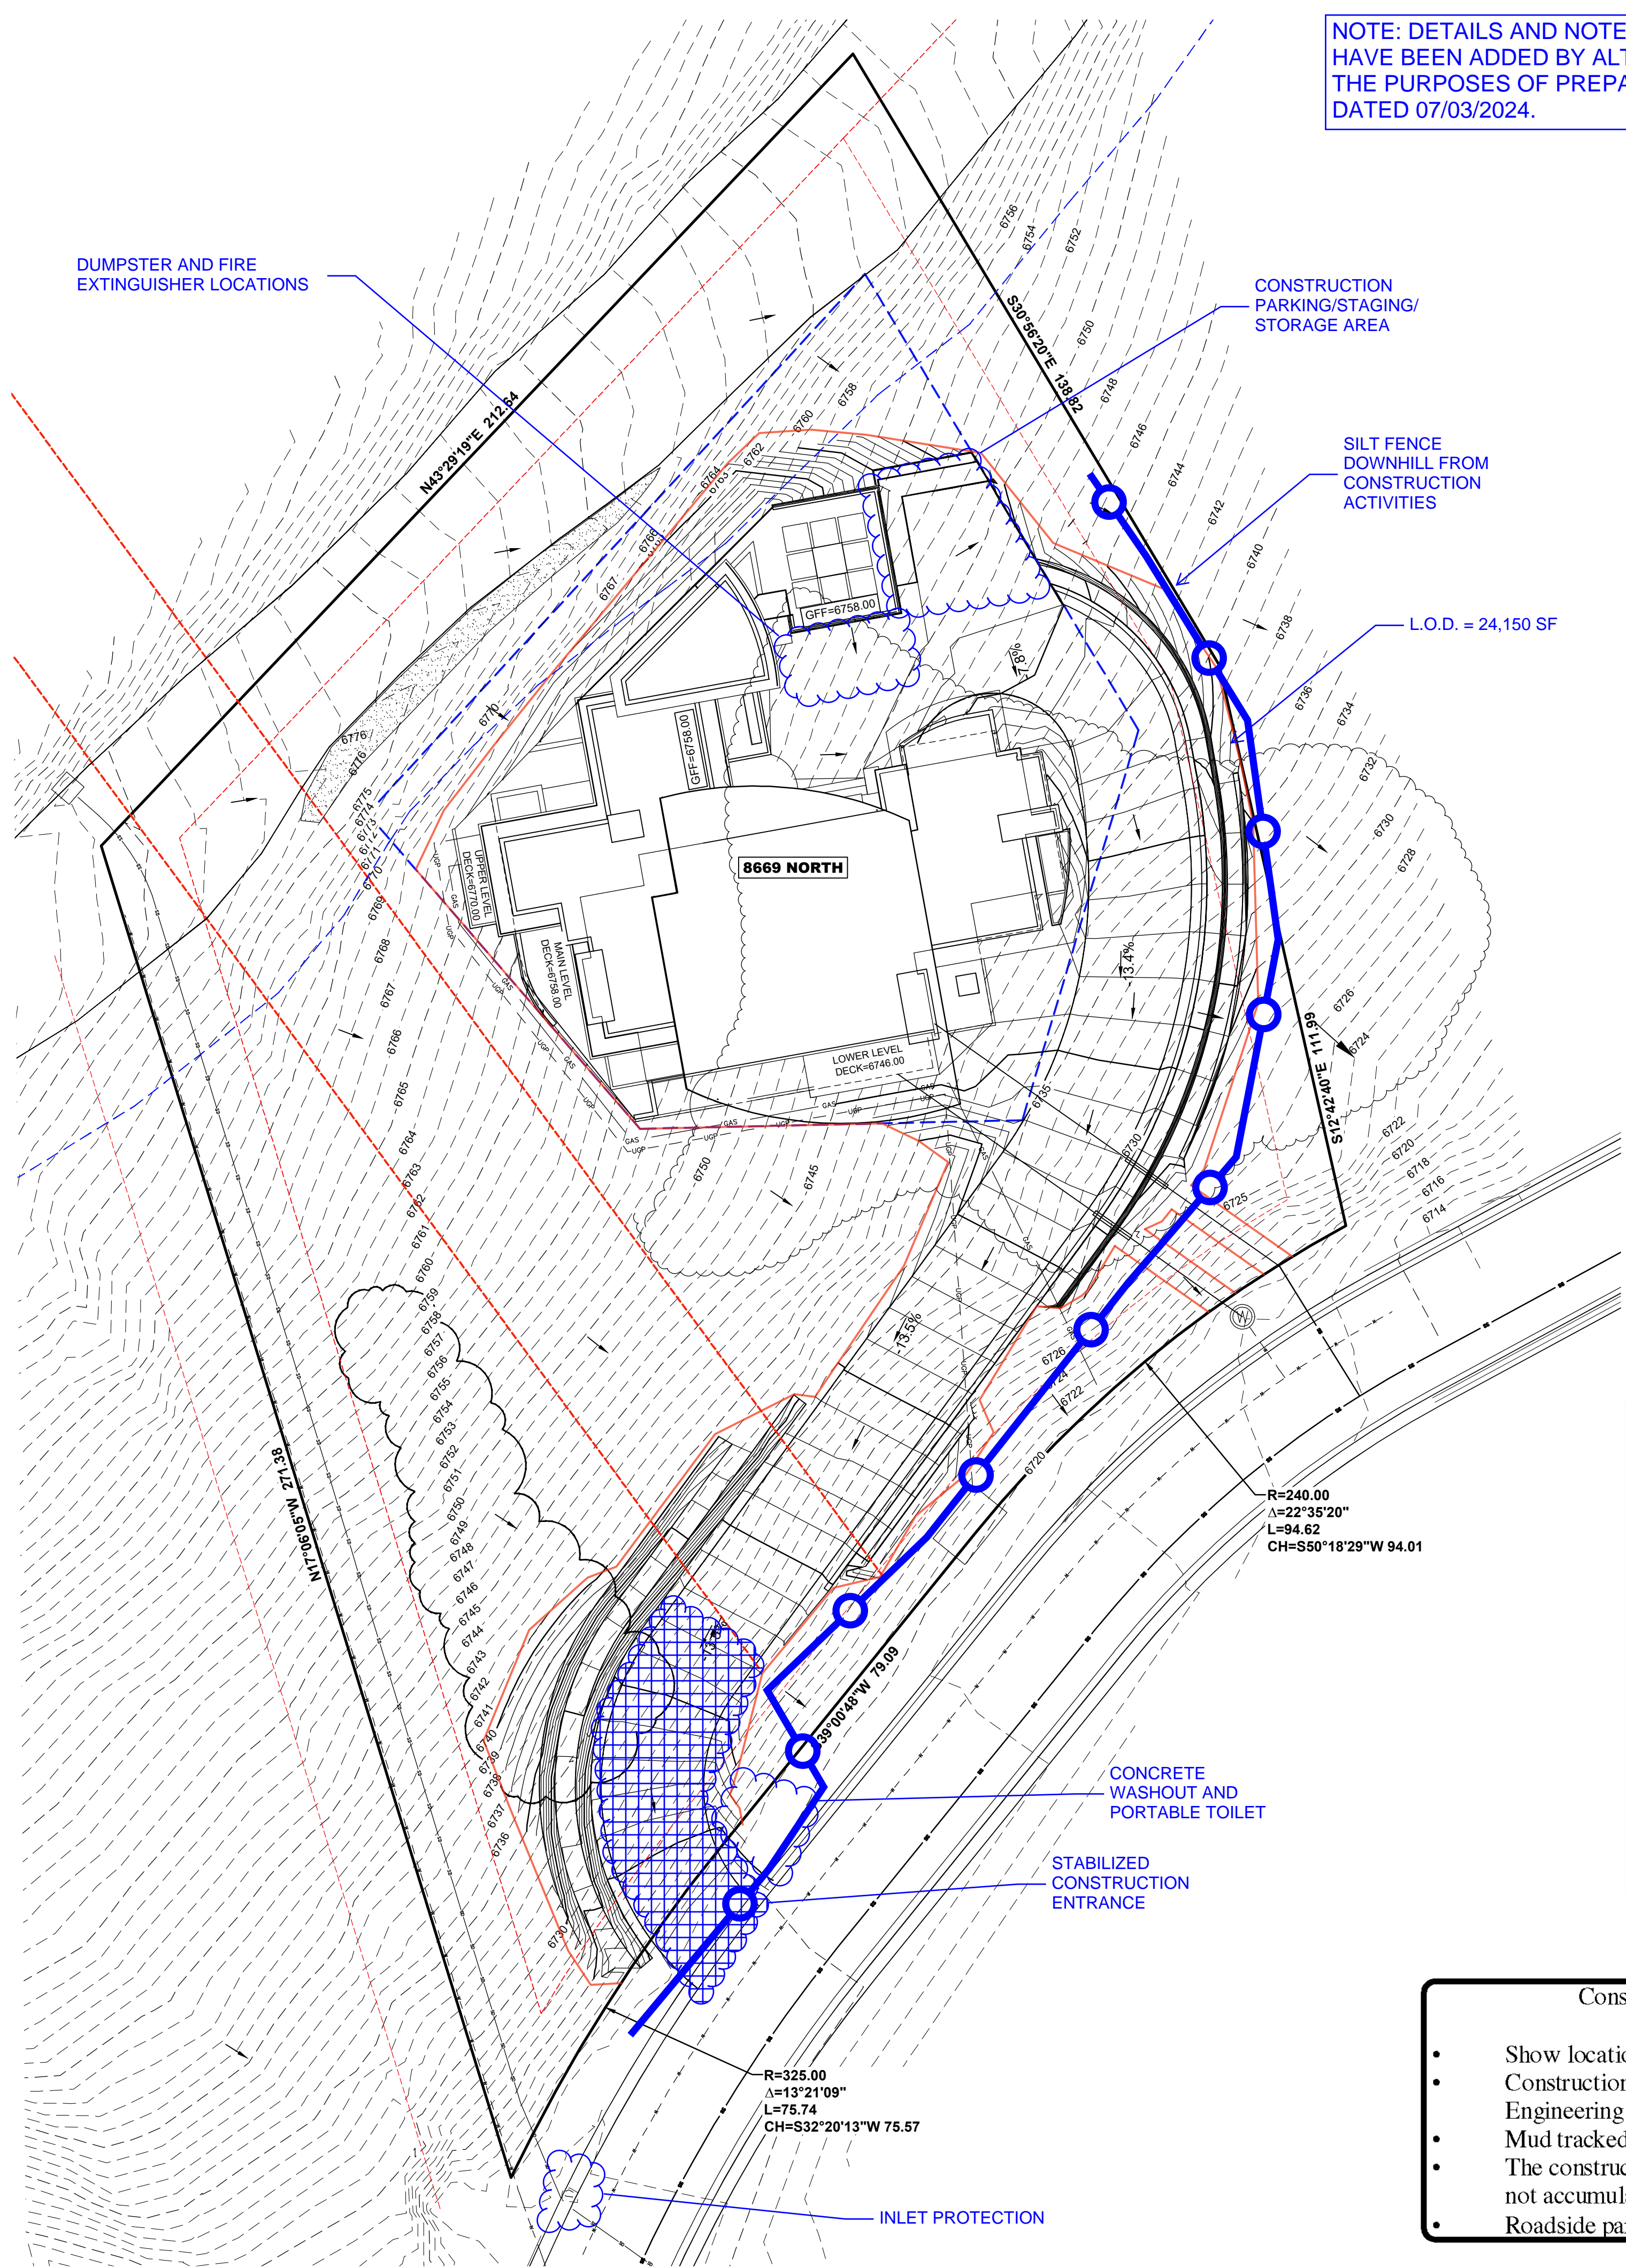

- Construction Mitigation Plan Notes**
- Show location for dumpster, portable toilets, materials storage, parking
 - Construction parking/traffic may not block the street without a permit (available from the Engineering Division)
 - Mud tracked out onto the street must be cleaned prior to the end of the work day
 - The construction site must be maintained in a neat manner. Trash and other debris may not accumulate outside the dumpster.
 - Roadside parking is not allowed from November 1st to April 1st

PINKERTON RESIDENCE
 MARCELLA LOT 7
GRADING AND DRAINAGE PLAN

REVISIONS

1	
2	
3	
4	
5	
6	

LEI PROJECT #:
2023-0052
 DRAWN BY:
BJA
 DESIGNED BY:
BTG
 SCALE:
1"=20'
 DATE:
3/14/2024

APPENDIX B: Common Plan Permit

Find the permit on <https://deq.utah.gov/water-quality/general-construction-storm-water-updes-permits>

APPENDIX C: Notice of Intent and Termination.

Find the Notice of Termination Form at <https://deq.utah.gov/water-quality/general-construction-storm-water-updes-permits>

However, termination of the project can be done on-line at <https://secure.utah.gov/stormwater>

(You must log in using the same username that you applied for your NOI with. If you completed a paper NOI you must complete a paper NOT.)



Notice of Intent (NOI) for Storm Water Discharges Associated with Construction
Activity Under the Common Plan Permit (CPP) UPDES General Permit
No. UTRH00000

NOI

Permit Information

Master Permit Number: UTRH00000
UPDES ID: UTRH08269
State/Territory to which your project/site is discharging: UT
Is your project/site located on federally recognized Indian Country Lands? No
Which type of form would you like to submit? Notice of Intent (NOI)
Have stormwater discharges from your project/site been covered previously under an UPDES permit? No
Has a Stormwater Pollution Prevention Plan (SWPPP) been prepared in advance of filling this NOI, as required? Yes

Owner/Operator Information

Owner Information

Owner: McNulty Construction
Status of Owner: Private
Owner Mailing Address:
Address Line 1: 1526 W Ute Blvd
Address Line 2: City: Park City
ZIP/Postal Code: 84098 State: UT

Owner Point of Contact Information

First Name Middle Initial Last Name: Mike McNulty
Title: Site Supervisor and Owner
Phone: 435-659-9765 Ext.:
Email: mike@mmconst.com

Operator Information

Is the Operator Information the same as the Owner Information? Yes


NOI Preparer Information

This NOI is being prepared by someone other than the certifier.

First Name Middle Initial Last Name: Blayde McIntire
Organization: Altitude Engineering
Phone: 307-679-8620 Ext.:
Email: blayde.mcintire@gmail.com

Project/Site Information

Project/Site Name: Marcella Lot 7
Project Number:
Project/Site Address
Address Line 1: 8669 N Ski Beach Way
Address Line 2: City: Heber City
ZIP/Postal Code: 84032 State: UT
County or Similar Division: Wasatch



We are very sorry, but it looks like we encountered a problem. undefined

Latitude/Longitude for the Project/Site

Coordinate System: Decimal Degrees

Latitude/Longitude: 40.615534°N, 111.442635°W

Estimated Project Start Date: 07/22/2024

Estimated Project End Date: 06/01/2026

Total Area of Plot (in Acres): 1.2

Estimated Area to be Disturbed (in Acres): 0.55

Proposed Best Management Practices

Silt Fence/Straw Wattle/Perimeter Controls

Seeding/Preservation of Vegetation

Proposed Good Housekeeping Practices

Sanitary/Portable Toilet

Washout Areas

Construction Chemicals/Building Supplies Storage Area

Garbage/Waste Disposal

Track Out Controls

Spill Control Measures

Site Activity Information

Municipal Separate Storm Sewer System (MS4) Operator Name: Not Applicable

Receiving Water Body: Jordanelle Reservoir

➤ This is known

What is the estimated distance to the nearest water body? 0.9

Unit: Miles

Is the receiving water designated as impaired? Yes

Will any part of the project area be located within 50 feet of any Water of the State? No

Does this project site have any other UPDES permits? No

Certification Information


I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I have no personal knowledge that the information submitted is other than true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations. Signing an electronic document on behalf of another person is subject to criminal, civil, administrative, or other lawful action.

Certified By: Mike McNulty

Certifier Title: Owner

Certifier Email: mike@mmconst.com

Certified On: 07/03/2024 4:02 PM ET



We are very sorry, but it looks like we encountered a problem. undefined

APPENDIX D: Daily Self-Inspection Log (permit part 3.2.2).

Storm Water Pollution Prevention Plan Template (SWPPP)
Common Plan Permit

Delegation of Authority

I, _____ (name), hereby designate the person or specifically described position below to be a duly authorized representative for the purpose of overseeing compliance with environmental requirements, including the Common Plan Permit, at the _____ construction site. The designee is authorized to sign any reports, stormwater pollution prevention plans and all other documents required by the permit.

_____ (name of person or position)

_____ (company)

_____ (address)

_____ (city, state, zip)

_____ (phone)

By signing this authorization, I confirm that I meet the requirements to make such a designation as set forth in _____ (Reference State Permit), and that the designee above meets the definition of a "duly authorized representative" as set forth in _____ (Reference State Permit).

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gathered and evaluated the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

Name:

Company:

Title:

Signature:

Date:

APPENDIX G: BMP Specifications and Details

See BMP Details attached on same sheet as Site Map in Appendix A.

Below are links to various Construction Storm Water BMP Manuals for reference.

Salt Lake County

http://slco.org/uploadedFiles/depot/publicWorks/engineering/final_bmp_constructi.pdf

BEST MANAGEMENT PRACTICES FOR CONSTRUCTION ACTIVITIES

Davis County

http://www.daviscountyutah.gov/docs/librariesprovider20/default-document-library/stormwater-best-management-practices.pdf?sfvrsn=c9cd4053_2

A Guide to Stormwater Best Management Practices

Nevada DOT

<https://www.nevadadot.com/home/showdocument?id=9417>

Stormwater Quality Manuals: Construction Site Best Management Practices (BMPs) Manual

Caltrans

<http://www.dot.ca.gov/hq/construc/stormwater/CSBMP-May-2017-Final.pdf>

Construction Site Best Management Practices (BMP) Manual

Oregon

<http://www.oregon.gov/deq/FilterPermitsDocs/BMPManual.pdf>

Construction Stormwater Best Management Practices Manual

Los Angeles

<http://dpw.lacounty.gov/cons/specs/BMPManual.pdf>

Construction Site Best Management Practices (BMPs) Manual

Maricopa County (Arizona)

<https://www.maricopa.gov/DocumentCenter/View/2368/2015-03-Drainage-Design-Manual-for-Maricopa-County-Volume-III-Erosion-pdf>

Drainage Design Manual for Maricopa County (Erosion Control)

Minnesota

<https://www.pca.state.mn.us/sites/default/files/wq-strm2-09.pdf>

Stormwater Compliance Assistance Toolkit for Small Construction Operators
